



(kV)		
230	15	TOTAL ENERGIZED
115	70	
%	83%	

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	669	600
WHITEFISH	5	5	123	123
COBRA	16	10	796	590
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	87	2004	1567

Status	Percentage
COBRA	44%
PREPA	38%
PENDING	19%

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing								
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish					
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38500	115	San Juan S.P. - Halo Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Cana - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38900	115	Escorial - Sabana Liana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37900	115	Encantada - Sabana Liana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%	
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%	
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%	
51000	230	Aguas Buenas - Sabana Liana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%	
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018. (2-Damages) on 2/19/2018.
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-STC) on 3/14/2018.
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%	n/a
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%	n/a
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%	
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%	n/a
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes		Yes	No	Yes	Yes	11/10/2017	1/20/2018	COMPLETED	✓	-	100%	Sleeves issue- Waiting on material. change to 1/17/18 pending material delivery
41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes		Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Master finish (8-STC, 12-Damages) on 02/9/2018. Cobra finish (26-STC, 5-Damages) on 02/14/2018.

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGWpartially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	8/24/2018	IN PROGRESS		2	99%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✓	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	8/24/2018	IN PROGRESS		7	75%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	8/17/2018	IN PROGRESS		8	98%	Removed from FLUOR scope. PUMA pending.		
36200	115	Daguao - Fajardo	PREPA	23	23	100%	19	19	100%	Yes	Yes	No	Yes	No	1/31/2018	8/9/2018	IN PROGRESS	✗	9	100%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/30/2018	IN PROGRESS		11	89%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/15/2018	IN PROGRESS		12	66%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. wa		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/23/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUORscope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUORscope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	9/30/2018	IN PROGRESS		17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018. Tu		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	11/15/2018			18	11%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	9/22/2018			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUORscope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				757	565		1247	1002															

COBRA	7
PREPA	6
PENDING	3
	16



Executive Report- Huracan Maria
Electric System Reestablishment Plan - Transmission Lines

DATE: 08/10/2018 - 8:42 AM

85% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	69
%	82%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	73
Totals	103	88

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	60	669	600
WHITEFISH	5	5	123	123
COBRA	16	10	796	590
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	88	2004	1567

(kV)	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators, Repairs/Restoration)		Overall %
	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	106	404	365	92%
115	650	459	843	637	73%
Totals	757	565	1247	1002	78%

% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF
ASSIGNMENTS

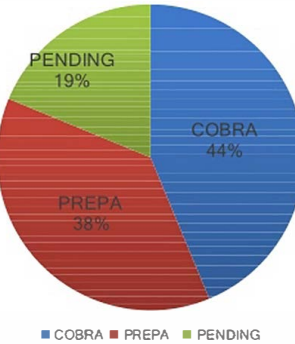

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish					COBRA	PREPA	PENDING
				Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)			Completed	Not Completed	Not Started	Not Yet Started			
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a		
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a		
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a		
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a		
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a		
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a		
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a		
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a		
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a		
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.		
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a		
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a		
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a		
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a		
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a		
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
50900	230	Agua Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable		
39000	115	Agua Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
39000	115	Comerio - Agua Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a		
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a		
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a		
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a		
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable		
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable		
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	n/a		
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%			
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%			
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%			
51000	230	Agua Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	11/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.		
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%			
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.		
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED						

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/11/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGWpartially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	8/23/2018	IN PROGRESS		2	86%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assign		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	8/24/2018	IN PROGRESS		7	75%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	8/17/2018	IN PROGRESS		8	98%	Removed from FLUOR scope. PUMA pending.		
36200	115	Daguao - Fajardo	PREPA	23	23	100%	19	19	100%	Yes	Yes	No	Yes	No	1/31/2018	8/9/2018	COMPLETED	✗	9	100%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/30/2018	IN PROGRESS		11	81%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/15/2018	IN PROGRESS		12	61%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. wa		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/23/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUORscope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUORscope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	9/30/2018	IN PROGRESS		17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018. Tu		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	10/20/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	9/22/2018			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUORscope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				757	565		1247	1002															

COBRA	7
PREPA	6
PENDING	3
	16



Executive Report- Huracan Maria
Electric System Reestablishment Plan - Transmission Lines

DATE: 08/10/2018 - 8:03 AM

85% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	69
%	82%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	73
Totals	103	88

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	60	669	600
WHITEFISH	5	5	123	123
COBRA	16	10	796	590
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	88	2004	1567

(kV)	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators, Repairs/Restoration)		Overall %
	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	106	404	365	92%
115	650	459	843	637	73%
Totals	757	565	1247	65.13604	31%

% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF
ASSIGNMENTS

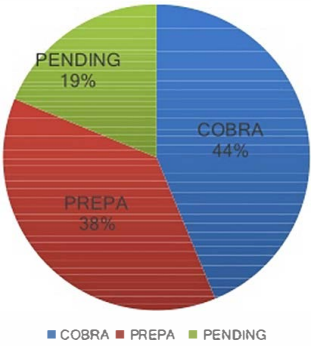

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
------	--------------	-----------	----------	---------------------	--	--	-----------------------	--	--	------------	--	--------------	--	----------------	--	-------	-----------------	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/11/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGWpartially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	8/23/2018	IN PROGRESS		2	86%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assign		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	8/24/2018	IN PROGRESS		7	75%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	8/17/2018	IN PROGRESS		8	98%	Removed from FLUOR scope. PUMA pending.		
36200	115	Daguao - Fajardo	PREPA	23	23	100%	19	19	100%	Yes	Yes	No	Yes	No	1/31/2018	8/9/2018	COMPLETED	✗	9	100%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/30/2018	IN PROGRESS		11	81%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/15/2018	IN PROGRESS		12	61%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. wa		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/23/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUORscope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUORscope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	9/30/2018	IN PROGRESS		17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018. Tu		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	10/20/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	9/22/2018			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUORscope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				757	565		1247	1002															

COBRA	7
PREPA	6
PENDING	3
	16



Executive Report- Huracan Maria
Electric System Reestablishment Plan - Transmission Lines

DATE: 08/17/2018 - 9:36 AM

85% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	70
%	83%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	73
Totals	103	88

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	60	669	600
WHITEFISH	5	5	123	123
COBRA	16	10	796	590
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	88	2004	1567

(kV)	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators, Repairs/Restoration)		Overall %
	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	106	404	365	92%
115	650	459	843	637	73%
Totals	757	565	1247	1002	78%

% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF
ASSIGNMENTS

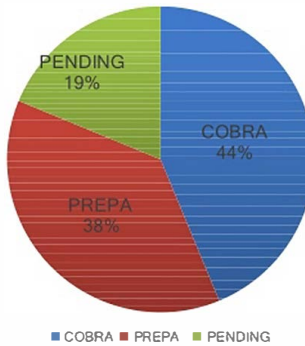

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish					COBRA	PREPA	PENDING	
				Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)			COMPLETED	IN-PROGRESS	TBD'S	100%				n/a
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a			
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a			
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a			
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a			
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a			
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a			
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a			
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a			
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a			
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.			
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a			
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a			
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a			
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a			
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a			
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
50900	230	Agua Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable			
39000	115	Agua Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
39000	115	Comerio - Agua Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a			
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a			
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a			
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a			
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable			
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable			
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	n/a			
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.			
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%				
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%				
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%				
51000	230	Agua Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	11/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.			
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes						1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.			
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes						2/14/2018	2/16/2018	COM							

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYP&A Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYP&A Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/11/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	8/23/2018	IN PROGRESS		2	86%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes					1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 4033		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✓	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	8/24/2018	IN PROGRESS		7	75%	Reprioritized by PREPA on Dec 27, 2017. Delayed due to PUMA.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	8/17/2018	IN PROGRESS		8	98%	Removed from FLUOR scope. Delayed due to PUMA.		
36200	115	Daguao - Fajardo	PREPA	23	23	100%	19	19	100%	Yes	Yes	No	Yes	No	1/31/2018	8/9/2018	COMPLETED	✗	9	100%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYP&A/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/30/2018	IN PROGRESS		11	82%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/15/2018	IN PROGRESS		12	61%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. wa		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/23/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	9/30/2018	IN PROGRESS		17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018. Tu		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	10/20/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	9/22/2018			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				757	565		1247	1002															

COBRA	7
PREPA	6
PENDING	3
	16



OVERALL PROGRESS
(As per completed Tasks)

70
830/

TOTAL ENERGIZED



				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing								
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish					
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-		9/22/2017	9/22/2017	COMPLETED	✓	-	100%
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-		9/23/2017	9/23/2017	COMPLETED	✓	-	100%
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-		9/26/2017	9/26/2017	COMPLETED	✓	-	100%
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-		9/23/2017	9/26/2017	COMPLETED	✓	-	100%
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-		9/23/2017	9/27/2017	COMPLETED	✓	-	100%
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-		9/28/2017	9/28/2017	COMPLETED	✓	-	100%
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-		9/23/2017	9/28/2017	COMPLETED	✓	-	100%
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-		9/28/2017	9/29/2017	COMPLETED	✓	-	100%
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-		9/29/2017	9/30/2017	COMPLETED	✓	-	100%
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-		9/30/2017	9/30/2017	COMPLETED	✓	-	100%
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-		9/27/2017	9/30/2017	COMPLETED	✓	-	100%
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-		9/27/2017	10/1/2017	COMPLETED	✓	-	100%
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-		10/1/2017	10/1/2017	COMPLETED	✓	-	100%
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-		9/29/2017	10/1/2017	COMPLETED	✓	-	100%
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-		10/2/2017	10/2/2017	COMPLETED	✓	-	100%
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-		10/3/2017	10/4/2017	COMPLETED	✓	-	100%
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-		9/28/2017	10/4/2017	COMPLETED	✓	-	100%
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-		9/27/2017	10/5/2017	COMPLETED	✓	-	100%
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-		10/4/2017	10/5/2017	COMPLETED	✓	-	100%
36100	115	Cana - Pinas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-		9/30/2017	10/8/2017	COMPLETED	✓	-	100%
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-		10/9/2017	10/13/2017	COMPLETED	✓	-	100%
36100	115	Pinas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-		10/9/2017	10/13/2017	COMPLETED	✓	-	100%
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-		10/7/2017	10/13/2017	COMPLETED	✓	-	100%
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-		10/7/2017	10/13/2017	COMPLETED	✓	-	100%
41500	115	Dorado TC - Pinas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-		9/26/2017	10/14/2017	COMPLETED	✓	-	100%
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-		10/11/2017	10/15/2017	COMPLETED	✓	-	100%
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-		10/11/2017	10/15/2017	COMPLETED	✓	-	100%
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-		10/11/2017	10/15/2017	COMPLETED	✓	-	100%
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-		10/11/2017	10/15/2017	COMPLETED	✓	-	100%
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-		10/13/2017	10/18/2017	COMPLETED	✓	-	100%
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-		10/11/2017	10/20/2017	COMPLETED	✓	-	100%
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-		9/27/2017	10/22/2017	COMPLETED	✓	-	100%
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-		9/28/2017	10/27/2017	COMPLETED	✓	-	100%
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-		10/26/2017	10/29/2017	COMPLETED	✓	-	100%
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-		11/1/2017	11/4/2017	COMPLETED	✓	-	100%
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-		9/27/2017	11/5/2017	COMPLETED	✓	-	100%
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-		10/20/2017	11/6/2017	COMPLETED	✓	-	100%
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-		11/9/2017	11/11/2017	COMPLETED	✓	-	100%
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-		11/9/2017	11/11/2017	COMPLETED	✓	-	100%
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-		11/9/2017	11/11/2017	COMPLETED	✓	-	100%
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-		11/2/2017	11/15/2017	COMPLETED	✓	-	100%
37400	115	Bayamon TC - Oea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-		10/31/2017	11/21/2017	COMPLETED	✓	-	100%
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-		11/10/2017	11/27/2017	COMPLETED	✓	-	100%
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-		11/10/2017	11/28/2017	COMPLETED	✓	-	100%
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-		11/3/2017	12/5/2017	COMPLETED	✓	-	100%
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-		11/9/2017	12/14/2017	COMPLETED	✓	-	100%
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-		11/18/2017	12/16/2017	COMPLETED	✓	-	100%
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No		12/4/2017	12/23/2017	COMPLETED	✓	-	100%
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No		11/20/2017	12/24/2017	COMPLETED	✓	-	100%
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No		12/6/2017	12/30/2017	COMPLETED	✓	-	100%
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No		10/28/2017	1/14/2018	COMPLETED	✓	-	100%
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-		1/27/2018	2/9/2018	COMPLETED	✓	-	100%
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-		2/14/2018	2/16/2018	COMPLETED	✓	-	100%
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No		11/29/2017	2/25/2018	COMPLETED	✓	-	100%
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No		12/18/2017	3/14/2018	COMPLETED	✓	-	100%
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No		1/16/2018	3/27/2018	COMPLETED	✓	-	100%
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-		10/13/2017	10/25/2017	COMPLETED	✓	-	100%
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-		10/14/2017	10/29/2017	COMPLETED	✓	-	100%
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-		10/19/2017	11/14/2017	COMPLETED	✓	-	100%
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-		10/11/2017	11/29/2017	COMPLETED	✓	-	100%
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-		10/23/2017	11/30/2017	COMPLETED	✓	-	100%
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes		-	-	-	-		11/16/2017	11/20/2017	COMPLETED	✓	-	100%
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-		11/21/2017	12/3/2017	COMPLETED	✓	-	100%
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-		11/21/2017	12/3/2017	COMPLETED	✓	-	100%
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-		10/31/2017	12/7/2017	COMPLETED	✓	-	100%
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes		Yes	No	Yes	Yes		11/10/2017	12/0/2018	COMPLETED	✓	-	100%
41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes		Yes	Yes	Yes	Yes		12/7/2017	2/21/2018	COMPLETED	✓	-	100%

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/11/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGWpartially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	8/23/2018	IN PROGRESS		2	86%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✓	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assign		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	8/24/2018	IN PROGRESS		7	75%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	8/17/2018	IN PROGRESS		8	98%	Removed from FLUOR scope. PUMA pending.		
36200	115	Daguao - Fajardo	PREPA	23	23	100%	19	19	100%	Yes	Yes	No	Yes	No	1/31/2018	8/9/2018	COMPLETED	✗	9	100%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPFA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/30/2018	IN PROGRESS		11	82%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/15/2018	IN PROGRESS		12	61%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. wa		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/23/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUORscope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUORscope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	9/30/2018	IN PROGRESS		17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018. Tu		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	10/20/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	9/22/2018			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUORscope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				757	565		1247	1002															

COBRA	7
PREPA	6
PENDING	3
	16



	TOTALS BY kV	
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	72
Totals	103	87

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	667	596
WHITEFISH	5	5	123	123
COBRA	16	10	796	590
NYP&A	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	87	2002	1563

(kV)	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall Repairs/Restoration %
	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	106	404	365	92%
115	648	456	843	636	73%
Totals	755	562	1247	65,08842	31%

Response	Percentage
COBRA	38%
PREPA	44%
PENDING	19%

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing									
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish						
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a	
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a	
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a	
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a	
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a	
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a	
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36100	115	Bayamon TC - Caná	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a	
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a	
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a	
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.	
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a	
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a	
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a	
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a	
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a	
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable	
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a	
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a	
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a	
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a	
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable	
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable	
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	n/a	
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%		
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%		
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%		
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.	
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%		
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.	
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018. (	
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-ST	
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%	n/a	
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%	n/a	
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable	
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%		
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%	n/a	
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes		Yes	No	Yes	Yes	11/10/2017	12/0/2018	COMPLETED	✓	-	100%	Sleeves issue. Waiting on material, change to 1/17/18 pending material delivery	
41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes		Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Mastec finish (8-STC, 1	

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	7/30/2018	IN PROGRESS		2	84%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	7/21/2018	IN PROGRESS		7	73%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	7/15/2018	IN PROGRESS		8	88%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.		
36200	115	Daguao - Fajardo	PREPA	21	20	95%	19	18	95%	Yes	Yes	No	Yes	No	1/31/2018	7/15/2018	IN PROGRESS		9	75%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPFA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC, 5		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/15/2018	IN PROGRESS		11	53%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/18/2018	IN PROGRESS		12	90%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/2/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	9/22/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				755	562		1247	1001															

COBRA	6
PREPA	7
PENDING	3
	16



Executive Report- Huracan Maria
Electric System Reestablishment Plan - Transmission Lines

DATE: 07/18/2018 - 3:15 PM

84% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	69
%	82%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	72
Totals	103	87

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	669	598
WHITEFISH	5	5	123	123
COBRA	16	10	796	590
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	87	2004	1565

(kV)	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators, Repairs/Restoration)		Overall %
	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	106	404	365	92%
115	650	457	843	637	73%
Totals	757	563	1247	65.04908	31%

% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF
ASSIGNMENTS

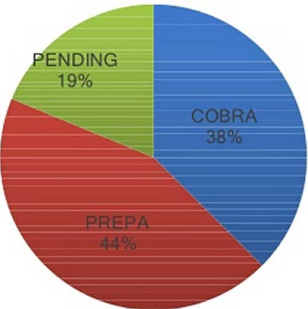

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish					Notes
				Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)			COMPLETED	IN-PROGRESS	TBD'S	Notes	
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100% n/a	
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100% n/a	
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100% n/a	
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100% n/a	
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100% n/a	
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100% n/a	
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100% n/a	
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100% n/a	
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100% n/a	
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100% Lightning arrester replaced. Tested OK.	
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100% n/a	
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100% n/a	
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100% n/a	
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100% n/a	
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100% n/a	
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
50900	230	Agua Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100% Energized without replacing damaged OPGW cable	
39000	115	Agua Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
39000	115	Comerio - Agua Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100% n/a	
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100% n/a	
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100% n/a	
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100% n/a	
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100% Energized without replacing damaged OPGW cable	
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100% Energized without replacing damaged OPGW cable	
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.	
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%	
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%	
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%	
51000	230	Agua Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	11/14/2018	COMPLETED	✓	-	100% OPGW installed. Currently working to replace damaged OPGW spans.	
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100% WX Permitting.	
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%	
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100% PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.	
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100% Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018.	
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100% OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-STC)	
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-		

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes		Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu	
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes		Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr	
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes		Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages). Pr	
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.	
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl	
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes		Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.	
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes		Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.	
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes		Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.	
36300	115	Shell TC/Juan Martin Sect.- Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes		Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2	
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes		Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018	
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes		Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.	
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes		Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas	
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes		Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.	
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes		Yes	No	Yes	No	10/17/2017	7/30/2018	IN PROGRESS		2	88%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo	
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes		Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.	
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331	
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes		Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig	
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes		Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done	
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes						3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz	
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes				Yes	No	2/19/2018	7/31/2018	IN PROGRESS		7	75%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.	
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes				Yes	No	3/24/2018	7/31/2018	IN PROGRESS		8	90%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.	
36200	115	Daguao - Fajardo	PREPA	23	21	91%	19	19	100%	Yes		Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	92%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar	
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes		Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,	
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes		Yes	Yes	Yes	No	11/3/2017	8/15/2018	IN PROGRESS		11	77%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa	
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes		Yes	No	Yes	No	1/28/2018	9/18/2018	IN PROGRESS		12	59%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.	
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes		Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.	
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes		Yes	No	Yes	No	1/18/2018	10/2/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.	
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes		Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.	
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes		Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem	
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes		Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.	
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes		No				2/21/2018	9/22/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.	
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No						3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope	
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes		Yes	No			4/24/2018	TBD			20	0%	For rebuild.	
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes		Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.	
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes		Yes	No			2/24/2018	TBD			22	0%	For rebuild.	
				757	563		1247	1002															

COBRA	6
PREPA	7
PENDING	3
	16



OVERALL PROGRESS
(As per completed Tasks)

69
000

TOTAL ENERGIZED



				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing								
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish					
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Bayamon TC - Caná	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Bayamon TC - Orea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	n/a
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%	n/a
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%	n/a
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%	n/a
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%	n/a
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018. (2-Damages) on 2/21/2018.
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-STC) on 3/14/2018.
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%	n/a
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%	n/a
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%	n/a
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%	n/a
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes		Yes	No	Yes	Yes	11/10/2017	1/20/2018	COMPLETED	✓	-	100%	Sleeves issue- Waiting on material. change to 1/17/18 pending material delivery
41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes		Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Mastec finish (8-STC, 12-Damages) on 02/9/2018. Cobra finish (26-STC, 5-Damages) on 02/14/2018.

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYP&A Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	7/30/2018	IN PROGRESS		2	84%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	7/21/2018	IN PROGRESS		7	74%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	7/15/2018	IN PROGRESS		8	88%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.		
36200	115	Daguao - Fajardo	PREPA	21	20	95%	19	19	100%	Yes	Yes	No	Yes	No	1/31/2018	7/15/2018	IN PROGRESS		9	90%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYP&A/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/15/2018	IN PROGRESS		11	53%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/18/2018	IN PROGRESS		12	90%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/2/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	9/22/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				755	562		1247	1002															

COBRA	6
PREPA	7
PENDING	3
	16

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/11/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	8/22/2018	IN PROGRESS		2	85%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	7/31/2018	IN PROGRESS		7	75%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	7/31/2018	IN PROGRESS		8	95%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.		
36200	115	Daguao - Fajardo	PREPA	23	21	91%	19	19	100%	Yes	Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	95%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPFA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/15/2018	IN PROGRESS		11	78%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/18/2018	IN PROGRESS		12	45%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/2/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	9/22/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				757	563		1247	1002															

COBRA	6
PREPA	7
PENDING	3
	16



Executive Report- Huracan Maria
Electric System Reestablishment Plan - Transmission Lines

DATE: 08/02/2018 - 7:11 PM

84% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	69
%	82%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	72
Totals	103	87

		TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
		LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
	PREPA	65	59	629	578
	WHITEFISH	5	5	123	123
	COBRA	17	10	836	610
	NYPA	3	3	15	15
	Fluor/PIKE	6	6	109	109
	Fluor/ARC	1	1	27	27
	Fluor/MasTec	0	0	0	0
	Fluor/SEC	1	1	25	25
	USACE/PowerSecure	2	2	32	32
	Pending-RFP	3	0	208	46
	Totals	103	87	2004	1565

		STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators, Repairs/Restoration %)	
(kV)		DOWN	REPAIRED	DEFICIENCY	REPAIRED
230		107	106	404	365
115		650	457	843	637
Totals		757	563	1247	65.04908
					31%

% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF
ASSIGNMENTS

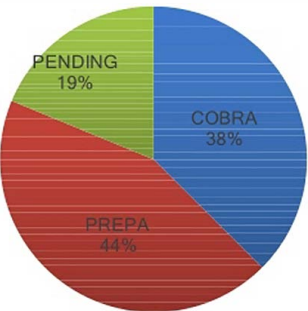

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish				
				Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)			COMPLETED	IN-PROGRESS	TBD'S	STATUS
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100% n/a
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100% n/a
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100% n/a
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100% n/a
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100% n/a
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100% n/a
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100% n/a
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100% n/a
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100% n/a
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100% Lightning arrester replaced. Tested OK.
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100% n/a
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100% n/a
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100% n/a
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100% n/a
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100% n/a
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
50900	230	Agua Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100% Energized without replacing damaged OPGW cable
39000	115	Agua Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
39000	115	Comerio - Agua Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100% n/a
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100% n/a
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100% n/a
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100% n/a
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100% Energized without replacing damaged OPGW cable
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100% Energized without replacing damaged OPGW cable
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%
51000	230	Agua Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	11/14/2018	COMPLETED	✓	-	100% OPGW installed. Currently working to replace damaged OPGW spans.
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100% WX Permitting.
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100% PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100% Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018.
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100% OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-STC)
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100% OPGW installed. Tested OK.
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19														

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYP&A Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYP&A Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	10	33%	Yes	Yes	No	Yes	No	10/17/2017	8/23/2018	IN PROGRESS		2	85%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	8/24/2018	IN PROGRESS		7	75%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	8/10/2018	IN PROGRESS		8	95%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.		
36200	115	Daguao - Fajardo	PREPA	23	21	91%	19	19	100%	Yes	Yes	No	Yes	No	1/31/2018	8/10/2018	IN PROGRESS		9	95%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYP&A/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/30/2018	IN PROGRESS		11	78%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/15/2018	IN PROGRESS		12	45%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/23/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	COBRA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	9/30/2018			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	10/20/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	9/22/2018			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				757	563		1247	1002															

COBRA	6
PREPA	7
PENDING	3
	16

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYP&A Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYP&A Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes	Yes	No	Yes	No	10/17/2017	7/30/2018	IN PROGRESS		2	95%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	7/21/2018	IN PROGRESS		7	73%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	7/15/2018	IN PROGRESS		8	88%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.		
36200	115	Daguao - Fajardo	PREPA	21	20	95%	19	18	95%	Yes	Yes	No	Yes	No	1/31/2018	7/15/2018	IN PROGRESS		9	75%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYP&A/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	8/15/2018	IN PROGRESS		11	91%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/18/2018	IN PROGRESS		12	42%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/2/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	9/22/2018			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				755	546		1247	993															

COBRA	6
PREPA	7
PENDING	3
	16



Executive Report- Huracan Maria Electric System Reestablishment Plan - Transmission Lines

DATE: 06/22/2018 - 9:19 PM

83% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	68
%	81%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	71
Totals	103	86

		TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
		LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
	PREPA	66	59	667	589
	WHITEFISH	5	5	123	123
	COBRA	16	9	796	560
	NYPA	3	3	15	15
	Fluor/PIKE	6	6	109	109
	Fluor/ARC	1	1	27	27
	Fluor/MasTec	0	0	0	0
	Fluor/SEC	1	1	25	25
	USACE/PowerSecure	2	2	32	32
	Pending-RFP	3	0	208	46
	Totals	103	86	2002	1526

		STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators, Repairs/Restoration %)	
(kV)		DOWN	REPAIRED	DEFICIENCY	REPAIRED
230		107	103	404	357
115		648	437	843	629
Totals		755	540	1247	63.86163
					30%

% WORK BREAKDOWN (COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF ASSIGNMENTS

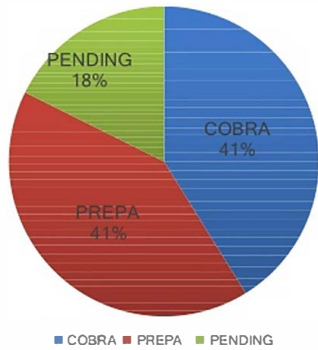

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish									
				Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)			COMPLETED	IN-PROGRESS	TBD'S	100%	n/a	OPGW installed. Tested OK.	OPGW installed. Tested OK.	OPGW installed. Tested OK.	OPGW installed. Tested OK.
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes	-	Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a				
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a				
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes	-	-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes	-	-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a				
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes	-	-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a				
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes	-	-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes	-	-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-	-	-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a				
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-	-	-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a				
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes	-	-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a				
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes	-	-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
36100	115	Cana - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes	-	-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a				
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-	-	-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a				
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-	-	-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes	-	-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes	-	-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a				
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a				
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a				
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-	-	-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a				
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes	-	-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a				
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes	-	-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
50900	230	Agua Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes	-	-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable				
39000	115	Agua Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes	-	-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
39000	115	Comerio - Agua Buenas	PREPA	1	1	100%	5	5	100%	Yes	-	-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a				
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes	-	-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a				
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes	-	-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a				
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a				
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-	-	-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes	-	-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable				
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes	-	-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable				
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes	-	-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%					
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes	-	-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes	-	-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.				
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes	-	Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%					
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes	-	Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%					
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes	-	Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%					
51000	230	Agua Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes	-	Yes	Yes	Yes	No	10/28/2017	11/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.				
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes	-	-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.				</

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes	Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	81%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes	Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS		3	99%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	5	83%	Yes			Yes	No	2/19/2018	6/29/2018	IN PROGRESS		7	67%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	6/29/2018	IN PROGRESS		8	83%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.		
36200	115	Daguao - Fajardo	PREPA	21	15	71%	19	17	89%	Yes	Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	58%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	50%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				755	540		1247	986															

COBRA	7
PREPA	7
PENDING	3
	17



Executive Report- Huracan Maria
Electric System Reestablishment Plan - Transmission Lines

DATE: 06/25/2018 - 5:25 PM

83% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	69
%	82%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	71
Totals	103	86

TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED			
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED	
	PREPA	66	59	667	589
	WHITEFISH	5	5	123	123
	COBRA	16	9	796	560
	NYPA	3	3	15	15
	Fluor/PIKE	6	6	109	109
	Fluor/ARC	1	1	27	27
	Fluor/MasTec	0	0	0	0
	Fluor/SEC	1	1	25	25
	USACE/PowerSecure	2	2	32	32
	Pending-RFP	3	0	208	46
	Totals	103	86	2002	1526

	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall
(kV)	DOWN	REPAIRED	DEFICIENCY	REPAIRED	Repairs/Restoration %
230	107	103	404	357	90%
115	648	437	843	629	71%
Totals	755	540	1247	63.86163	30%

% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF
ASSIGNMENTS

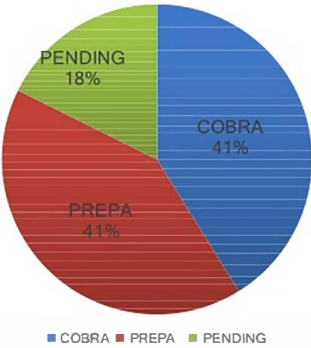

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish	Status	Remarks	Completion %	Notes	
				Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)							
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes	-	Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38500	115	San Juan S.P. - Halo Rey TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes	-	-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes	-	-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes	-	-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes	-	-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes	-	-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-	-	-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-	-	-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes	-	-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes	-	-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Cana - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes	-	-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-	-	-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-	-	-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes	-	-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes	-	-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-	-	-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes	-	-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes	-	-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50900	230	Agua Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes	-	-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
39000	115	Agua Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes	-	-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Comerio - Agua Buenas	PREPA	1	1	100%	5	5	100%	Yes	-	-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes	-	-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes	-	-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-	-	-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes	-	-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes	-	-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes	-	-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	-
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes	-	-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes	-	-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes	-	Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%	-
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes	-	Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%	-
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes	-	Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%	-
51000	230	Agua Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes	-	Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes	-	-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes	-	-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%	-
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes	-	Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/15/2018.
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes	-	Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018.
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes	-	Yes	Yes	Yes	No	1/16/2018	3/27/2018					

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGWpartially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes	Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	81%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes	Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS		3	99%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	5	83%	Yes			Yes	No	2/19/2018	6/29/2018	IN PROGRESS		7	67%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	6/29/2018	IN PROGRESS		8	83%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.		
36200	115	Daguao - Fajardo	PREPA	21	15	71%	19	17	89%	Yes	Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	58%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPFA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	50%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUORscope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				755	540		1247	986															

COBRA	7
PREPA	7
PENDING	3
	17



	TOTALS BY kV	
(kV)	LINESEGMENT	COMPLETED
230	17	15
115	86	72
Totals	103	87

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	667	594
WHITEFISH	5	5	123	123
COBRA	16	10	796	566
NYP&A	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/M&S Tec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	87	2002	1537


	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall Repairs/Restoration %
(kV)	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	103	404	357	90%
115	648	442	843	635	72%
Totals	755	545	1247	64,38544	30%

Response	Percentage
COBRA	38%
PREPA	44%
PENDING	19%

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing										
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish							
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a		
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a		
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a		
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a		
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a		
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a		
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a		
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36100	115	Cana - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a		
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a		
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.		
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a		
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a		
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a		
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a		
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a		
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable		
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a		
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a		
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a		
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a		
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37400	115	Bayamon TC - Orea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable		
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable		
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	n/a		
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%			
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%			
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%			
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.		
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%			
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.		
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018. (2-Damages) on 2/19/2018.		
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-STC) on 3/1/2018.		
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%	n/a		
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%	n/a		
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable		
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%			
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%	n/a		
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.		
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes														

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes		Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu	
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes		Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYP&A Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages), Pr	
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes		Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYP&A Finish (18-STC, 46-Damages). Pr	
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.	
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl	
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes		Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.	
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes		Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.	
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes		Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.	
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes		Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2	
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes		Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018	
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes		Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.	
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes		Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas	
50700	230	Gua yama/ A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes		Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.	
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes		Yes	No	Yes	No	10/17/2017	TBD	IN PROGRESS		2	83%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo	
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes		Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.	
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331	
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes		Yes	No	Yes	No	1/28/2018	6/30/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig	
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes		Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done	
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes						3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz	
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes				Yes	No	2/19/2018	7/21/2018	IN PROGRESS		7	72%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.	
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes				Yes	No	3/24/2018	7/15/2018	IN PROGRESS		8	87%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.	
36200	115	Daguao - Fajardo	PREPA	21	19	90%	19	17	89%	Yes		Yes	No	Yes	No	1/31/2018	7/15/2018	IN PROGRESS		9	72%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar	
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes		Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYP&A/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,	
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes		Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	52%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa	
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes		Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	42%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.	
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes		Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.	
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes		Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUORscope.	
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes		Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.	
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes		Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem	
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes		Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.	
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes		No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.	
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No						3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUORscope	
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes		Yes	No			4/24/2018	TBD			20	0%	For rebuild.	
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes		Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.	
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes		Yes	No			2/24/2018	TBD			22	0%	For rebuild.	
				755	545		1247	992															

COBRA	6
PREPA	7
PENDING	3
	16



(kV)		
230	15	TOTAL ENERGIZED
115	68	
%	81%	

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	667	578
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	86	2002	1515

	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall
(kV)	DOWN	REPAIRED	DEFICIENCY	REPAIRED	Repair/Restoration %
230	107	103	404	357	90%
115	648	430	843	625	71%
Totals	755	533	1247	63,22354	30%

A pie chart showing the distribution of responses for Question 1. The chart is divided into three segments: COBRA (41%), PREPA (41%), and PENDING (18%). A legend at the bottom identifies the colors: blue for COBRA, red for PREPA, and green for PENDING.

Response	Percentage
COBRA	41%
PREPA	41%
PENDING	18%

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing								
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish					
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50300	230	Aguirre S. P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Cana - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/28/2017	10/14/2017	COMPLETED	✓	-	100%	n/a
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a
38900	115	Marlin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%	
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%	
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%	
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%	
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/18
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018.
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-STU
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%	n/a
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%	n/a
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%	
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%	n/a
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes		Yes	No	Yes	Yes	11/10/2017	1/20/2018	COMPLETED	✓	-	100%	Sleeves issue. Waiting on material, change to 1/17/18 pending material delivery

41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes	Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Mastec finish (8-STC, 12-Damages) on 02/9/2018. Cobra finish (26-STC, 5-Damages) on 02/15/2018.				
50800	230	Yabucoa - Sabana Liana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Fluor/COBRA-Proposed finish date was 2/28/2018. Turnover to PREPA 02/23/2018.				
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No	Yes	No	11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages), PREPA priority.				
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages) on 02/15/2018.				
41200	115	Sabana Liana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.				
36800	115	Sabana Liana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.				
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to complete work on 3/8/18.				
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.				
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.				
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.				
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2/24/2018.				
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018				
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.				
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas.				
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.				
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes	Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS	✓	2	80%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previous to 6/29/2018.				
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done. Line tested ok.				
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331.				
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes	Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS	✓	3	99%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done.				
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done.				
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energized.				
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	5	83%	Yes			Yes	No	2/19/2018	6/29/2018	IN PROGRESS		7	60%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.				
39000	115	Toro Negro - Barranquitas	PREPA	5	1	20%	4	4	100%	Yes			Yes	No	3/24/2018	6/29/2018	IN PROGRESS		8	80%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.				
36200	115	Daguao - Fajardo	PREPA	21	10	48%	19	13	68%	Yes	Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	26%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Damages).				
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC, 1-Damage).				
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	49%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date was 2/28/2018.				
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.				
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.				
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.				
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.				
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Remaining work.				
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.				
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.				
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope.				
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.				
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.				
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.				
				755	533		1247	982																	

COBRA	7
PREPA	7
PENDING	3
	17



Executive Report- Huracan Maria
Electric System Reestablishment Plan - Transmission Lines

DATE: 06/27/2018 - 9:42 PM

84% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	69
%	82%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	72
Totals	103	87

		TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
		LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
	PREPA	66	59	667	592
	WHITEFISH	5	5	123	123
	COBRA	16	10	796	566
	NYPA	3	3	15	15
	Fluor/PIKE	6	6	109	109
	Fluor/ARC	1	1	27	27
	Fluor/Mas Tec	0	0	0	0
	Fluor/SEC	1	1	25	25
	USACE/PowerSecure	2	2	32	32
	Pending-RFP	3	0	208	46
	Totals	103	87	2002	1535

		STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall Repairs/Restoration %
(kV)		DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230		107	103	404	357	90%
115		648	440	843	635	72%
Totals		755	543	1247	64.29021	30%

% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF
ASSIGNMENTS

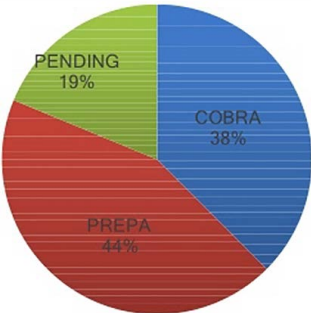

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish														
				Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)			COMPLETED	IN-PROGRESS	TBD'S	100%	90%	80%	70%	60%	50%	40%	30%	20%	10%	0%
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes	-	Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a									
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a									
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes	-	-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes	-	-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a									
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes	-	-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a									
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes	-	-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes	-	-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-	-	-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a									
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-	-	-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a									
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
36100	115	Bayamon TC - Caná	PREPA	6	6	100%	4	4	100%	Yes	-	-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a									
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes	-	-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes	-	-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a									
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-	-	-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a									
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-	-	-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes	-	-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes	-	-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a									
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a									
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a									
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-	-	-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a									
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes	-	-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a									
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes	-	-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
50900	230	Agua Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes	-	-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable									
39000	115	Agua Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes	-	-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
39000	115	Comerio - Agua Buenas	PREPA	1	1	100%	5	5	100%	Yes	-	-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a									
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes	-	-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a									
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes	-	-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a									
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a									
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-	-	-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes	-	-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable									
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes	-	-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable									
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes	-	-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%										
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes	-	-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes	-	-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.									

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYP&A Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYP&A Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama/ A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes	Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	82%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	6/30/2018	COMPLETED	✗	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	6	100%	Yes			Yes	No	2/19/2018	6/29/2018	IN PROGRESS		7	70%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.		
39000	115	Toro Negro - Barranquitas	PREPA	5	3	60%	4	4	100%	Yes			Yes	No	3/24/2018	6/29/2018	IN PROGRESS		8	85%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.		
36200	115	Daguao - Fajardo	PREPA	21	17	81%	19	17	89%	Yes	Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	68%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYP&A/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	52%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguo	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				755	543		1247	992															

COBRA	6
PREPA	7
PENDING	3
	16




OVERALL PROGRESS
(As per completed Tasks)

TOTAL ENERGIZED



	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNMENT	COMPLETED
PREPA	66	59	667	584
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	86	2002	1521

**% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)**

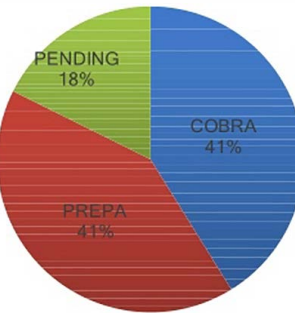

■ COBRA ■ PREPA ■ PENDING

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing									
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish						
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a	
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a	
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a	
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a	
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a	
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a	
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a	
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36100	115	Cana - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a	
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a	
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%		

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes		Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu	
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes		Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages), Pr	
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes		Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages). Pr	
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.	
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl	
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes		Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.	
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes		Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.	
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes		Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.	
36300	115	Shell TC/Juan Martin Sect.- Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes		Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2	
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes		Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018	
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes		Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.	
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes		Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas	
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes		Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.	
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes		Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	80%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo	
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes		Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.	
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331	
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes		Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS		3	99%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig	
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes		Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done	
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes						3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz	
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	5	83%	Yes				Yes	No	2/19/2018	6/29/2018	IN PROGRESS		7	65%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.	
39000	115	Toro Negro - Barranquitas	PREPA	5	2	40%	4	4	100%	Yes				Yes	No	3/24/2018	6/29/2018	IN PROGRESS		8	82%	Removed from FLUOR scope. Wire stringing from T-179 to T-182.	
36200	115	Daguao - Fajardo	PREPA	21	13	62%	19	15	79%	Yes		Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	48%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar	
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes		Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,	
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes		Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	49%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa	
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes		Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.	
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes		Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.	
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes		Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.	
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes		Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.	
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes		Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem	
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes		Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.	
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes		No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.	
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No						3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope	
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes		Yes	No			4/24/2018	TBD			20	0%	For rebuild.	
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes		Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.	
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes		Yes	No			2/24/2018	TBD			22	0%	For rebuild.	
				755	537		1247	984															

COBRA	7
PREPA	7
PENDING	3
	17



OVERALL PROGRESS
(As per completed Tasks)

68
81%

TOTAL ENERGIZED

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	657	560
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	86	1992	1497

Status	Percentage
COBRA	41%
PREPA	41%
PENDING	18%

[illegible]

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYP&A Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages), Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYP&A Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes	Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	70%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes	Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS		3	80%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	No					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	0	0%	No					2/19/2018	6/22/2018	IN PROGRESS		7	47%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly		
39000	115	Toro Negro - Barranquitas	PREPA	5	0	0%	1	0	0%	No					3/24/2018	6/29/2018	IN PROGRESS		8	40%	Removed from FLUOR scope. Tower assembly		
36200	115	Daguao - Fajardo	PREPA	21	9	43%	12	6	50%	Yes	Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	8%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope. 06/01/2018 Pl		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYP&A/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	45%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				755	531		1237	966															

COBRA	7
PREPA	7
PENDING	3
	17



Executive Report- Huracan Maria
Electric System Reestablishment Plan - Transmission Lines

DATE: 06/15/2018 - 5:41 PM

83% OVERALL PROGRESS (As per completed Tasks)	
(kV)	
230	15
115	68
%	81%
TOTAL ENERGIZED	


TOTALS BY kV		
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	71
Totals	103	86

		TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
		LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
	PREPA	66	59	667	578
	WHITEFISH	5	5	123	123
	COBRA	16	9	796	560
	NYPA	3	3	15	15
	Fluor/PIKE	6	6	109	109
	Fluor/ARC	1	1	27	27
	Fluor/Mas Tec	0	0	0	0
	Fluor/SEC	1	1	25	25
	USACE/PowerSecure	2	2	32	32
	Pending-RFP	3	0	208	46
	Totals	103	86	2002	1515

		STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall Repairs/Restoration %
(kV)		DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230		107	103	404	357	90%
115		648	430	843	625	71%
Totals		755	533	1247	63.22354	30%

% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)

% CURRENT STATE OF
ASSIGNMENTS

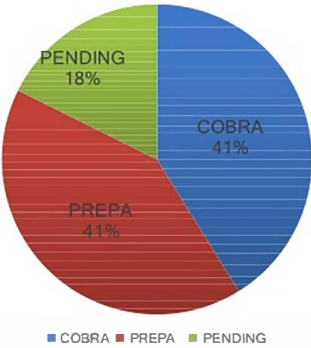

Line	Voltage (kV)	Task Name	Resource	Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing		Start	Proposed Finish																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
------	--------------	-----------	----------	---------------------	--	--	-----------------------	--	--	------------	--	--------------	--	----------------	--	-------	-----------------	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes		Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu	
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes		Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr	
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes		Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages). Pr	
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.	
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl	
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes		Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.	
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes		Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.	
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes		Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.	
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes		Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2/	
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes		Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018	
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes		Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.	
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes		Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas	
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes		Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGWpartially installed.	
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes		Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	80%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment. Previo	
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes		Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.	
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331	
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes		Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS		3	98%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assign	
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes		Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done	
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes						3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz	
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	5	83%	Yes				Yes	No	2/19/2018	6/22/2018	IN PROGRESS		7	55%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly	
39000	115	Toro Negro - Barranquitas	PREPA	5	1	20%	4	4	100%	Yes				Yes	No	3/24/2018	6/29/2018	IN PROGRESS		8	46%	Removed from FLUOR scope. Tower assembly	
36200	115	Daguao - Fajardo	PREPA	21	10	48%	19	13	68%	Yes		Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	15%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar	
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes		Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPFA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,	
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes		Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	49%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa	
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes		Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.	
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes		Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.	
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes		Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUORscope.	
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes		Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.	
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes		Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20Kft. static wire - May energize & install static later. Rem	
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes		Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.	
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes		No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.	
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No						3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUORscope	
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes		Yes	No			4/24/2018	TBD			20	0%	For rebuild.	
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes		Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.	
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes		Yes	No			2/24/2018	TBD			22	0%	For rebuild.	
				755	533		1247	982															

COBRA	7
PREPA	7
PENDING	3
	17



(kV)		
230	15	TOTAL ENERGIZED
115	68	
%	81%	

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	667	578
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	86	2002	1515

(kV)	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators, Repairs/Restoration etc.		Overall
	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	103	404	357	90%
115	648	430	843	625	71%
Totals	755	533	1247	63.22354	30%

Response	Percentage
COBRA	41%
PREPA	41%
PENDING	18%

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing								
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE/PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish					
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes	-	Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a
40300	115	Pattem - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
40300	115	Ponce TC - Pattem	PREPA	0	0	n/a	2	2	100%	Yes	-	-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes	-	-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes	-	-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes	-	-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes	-	-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-	-	-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-	-	-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-	-	-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Bayamon TC - Caná	PREPA	6	6	100%	4	4	100%	Yes	-	-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes	-	-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes	-	-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-	-	-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-	-	-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes	-	-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes	-	-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes	-	-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-	-	-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes	-	-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes	-	-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes	-	-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes	-	-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes	-	-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes	-	-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes	-	-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes	-	-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-	-	-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Bayamon TC - Orea TC	PREPA	2	2	100%	4	4	100%	Yes	-	-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes	-	-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes	-	-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	n/a
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes	-	-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes	-	-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes	-	-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes	-	Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%	n/a
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes	-	Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%	n/a
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes	-	Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%	n/a
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes	-	Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes	-	-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes	-	-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%	n/a
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes	-	Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes	-	Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018. (2-Damages) on 2/21/2018.
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes	-	Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-STC) on 2/21/2018.
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes	-	-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes	-	-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%	n/a
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes	-	-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%	n/a
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes	-	-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes	-	-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%	n/a
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes	-	-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%	n/a
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes	-	-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes	-	-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes	-	-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes	-	Yes	No	Yes	Yes	11/10/2017	1/20/2018	COMPLETED	✓	-	100%	Sleeves issue- Waiting on material, change to 1/17/18 pending material delivery
41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes	-	Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Mastec finish (8-STC, 12-Damages) on 02/9/2018. Cobra finish (26-STC, 5-Damages) on 02/9/2018.

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes		Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu	
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes		Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr	
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes		Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages). Pr	
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.	
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl	
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes		Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.	
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes		Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/28/2018.	
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes		Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.	
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes		Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2	
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes		Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018	
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes		Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.	
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes		Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas	
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes		Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.	
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes		Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	79%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo	
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes		Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.	
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 4033	
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes		Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS		3	91%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig	
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes		Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done	
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes						3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz	
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	5	83%	Yes				Yes	No	2/19/2018	6/22/2018	IN PROGRESS		7	55%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly	
39000	115	Toro Negro - Barranquitas	PREPA	5	1	20%	4	4	100%	Yes				Yes	No	3/24/2018	6/29/2018	IN PROGRESS		8	46%	Removed from FLUOR scope. Tower assembly	
36200	115	Daguao - Fajardo	PREPA	21	10	48%	19	13	68%	Yes		Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	15%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar	
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes		Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPFA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,	
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes		Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	48%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa	
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes		Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.	
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes		Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.	
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes		Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.	
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes		Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.	
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes		Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem	
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes		Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.	
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes		No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.	
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No						3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope	
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes		Yes	No			4/24/2018	TBD			20	0%	For rebuild.	
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes		Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.	
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes		Yes	No			2/24/2018	TBD			22	0%	For rebuild.	
				755	533		1247	982															

COBRA	7
PREPA	7
PENDING	3
	17



(kV)		
230	15	TOTAL ENERGIZED
115	67	
%	80%	


	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	657	560
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	86	1992	1497

Programa	Porcentaje
COBRA	41%
PREPA	41%
PENDING	18%

[illegible]

41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes	Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Mastec finish (8-STC, 12-Damages) on 02/9/2018. Cobra finish (26-STC, 5-Damages) on 02/9/2018.				
50800	230	Yabucoa - Sabana Liana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Fluor/COBRA-Proposed finish date was 2/28/2018. Turnover to PREPA 02/27/2018.				
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No	Yes	No	11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages), PREPA is working (3-STC, 5-Damages) on 2/7/2018.				
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages) on 2/7/2018. Turnover to PREPA 02/27/2018.				
41200	115	Sabana Liana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.				
36800	115	Sabana Liana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.				
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to complete OPGW installation.				
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.				
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.				
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.				
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2/24/2018.				
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018				
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.				
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas is working on repair.				
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.				
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes	Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS	✓	2	70%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previous to 6/29/2018.				
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done. Line tested ok.				
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331.				
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes	Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS	✓	3	80%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done.				
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done.				
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	No					3/24/2018	5/31/2018	COMPLETED	✗	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018.				
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	0	0%	No					2/19/2018	6/15/2018	IN PROGRESS		7	43%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly				
39000	115	Toro Negro - Barranquitas	PREPA	5	0	0%	1	0	0%	No					3/24/2018	6/15/2018	IN PROGRESS		8	34%	Removed from FLUOR scope. Tower assembly				
36200	115	Daguao - Fajardo	PREPA	21	9	43%	12	6	50%	Yes	Yes	No	Yes	No	1/31/2018	TBD	IN PROGRESS		9	3%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope. 06/01/2018 PREPA is working on repair.				
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC, 1-Damage) on 2/21/2018. Proposed finish date was 2/28/2018. Turnover to PREPA 02/27/2018.				
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	45%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date was 2/28/2018. Turnover to PREPA 02/27/2018.				
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.				
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.				
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.				
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.				
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Remaining work to be completed by PREPA.				
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.				
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.				
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope.				
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.				
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.				
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.				
				755	531		1237	966																	

COBRA	7
PREPA	7
PENDING	3
	17



OVERALL PROGRESS
(As per completed Tasks)

TOTAL ENERGIZED


	TOTALS BY KV	
(KV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	71
Totals	103	86

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	657	560
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	86	1992	1497

	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall
(kV)	DOWN	REPAIRED	DEFICIENCY	REPAIRED	Repair/Restoration %
230	107	103	404	357	90%
115	648	428	833	609	70%
Totals	755	531	1237	62,97592	30%

**% WORK BREAKDOWN
(COMPLETED/IN-PROGRESS/TBD'S)**

% CURRENT STATE OF ASSIGNMENTS

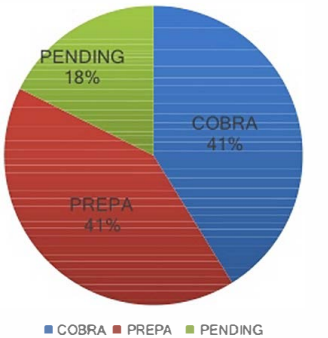

			Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing								
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish				
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%
50300	230	Aguirre S. P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%
36100	115	Bayamon TC - Cana	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%
36100	115	Cana - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/28/2017	10/14/2017	COMPLETED	✓	-	100%
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%
37400	115	Bayamon TC - Crea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes		Yes	No	Yes	Yes	11/10/2017	1/20/2018	COMPLETED	✓	-	100%

41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes		Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Mastec finish (8-STC, 12-Damages) on 02/9/2018. Cobra finish (26-STC, 5-Damages) on 02/9/2018.			
50800	230	Yabucoa - Sabana Liana	COBRA	7	7	100%	107	107	100%	Yes		Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Fluor Corp. removed from scope.			
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes		Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages), PREPA is working (3-STC, 5-Damages).			
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes		Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages) on 2/15/2018.			
41200	115	Sabana Liana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.			
36800	115	Sabana Liana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.			
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to complete work on 3/8/18.			
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes		Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.			
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes		Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.			
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes		Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.			
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes		Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2/21/2018.			
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes		Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018			
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes		Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.			
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes		Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas is working.			
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes		Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.			
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes		Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS	✓	2	70%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previous to 6/29/2018.			
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes		Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done. Line tested ok.			
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331.			
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes		Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS	✓	3	80%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assigned to PREPA.			
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes		Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done.			
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	No						3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energized.			
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	0	0%	No						2/19/2018	6/15/2018	IN PROGRESS		7	45%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly.			
39000	115	Toro Negro - Barranquitas	PREPA	5	0	0%	1	0	0%	No						3/24/2018	6/15/2018	IN PROGRESS		8	37%	Removed from FLUOR scope. Tower assembly.			
36200	115	Daguao - Fajardo	PREPA	21	9	43%	12	6	50%	Yes		Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	4%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope. 06/01/2018 PI.			
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes		Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC, 1-Damage) on 02/21/2018.			
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes		Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	45%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date was 2/28/2018.			
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes		Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.			
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes		Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.			
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes		Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.			
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes		Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.			
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes		Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem.			
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes		Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.			
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes		No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.			
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No						3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope.			
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes		Yes	No			4/24/2018	TBD			20	0%	For rebuild.			
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes		Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.			
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes		Yes	No			2/24/2018	TBD			22	0%	For rebuild.			
				755	531		1237	966																	

COBRA	7
PREPA	7
PENDING	3
	17




	TOTALS BY kV	
(kV)	LINE SEGMENT	COMPLETED
230	17	15
115	86	71
Totals	103	86

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNED	COMPLETED
PREPA	66	59	657	560
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYP&A	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	86	1992	1497

	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall Repairs/Restoration %
(kV)	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	103	404	357	90%
115	648	428	833	609	70%
Totals	755	531	1237	62.97592	30%

% CURRENT STATE OF ASSIGNMENTS

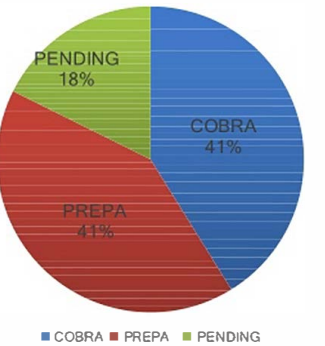

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing								
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish					
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Bayamon TC - Caná	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Bayamon TC - Orea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	n/a
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%	n/a
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%	n/a
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%	n/a
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%	n/a
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/2018.
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018. (2-Damages) on 2/19/2018.
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-STC) on 3/1/2018.
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%	n/a
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%	n/a
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%	n/a
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%	n/a
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes		Yes	No	Yes	Yes	11/10/2017	12/0/2018	COMPLETED	✓	-	100%	Sleeves issue. Waiting on material, change to 1/17/18 pending material delivery
41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes		Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Master finish (8-STC, 12-Damages) on 02/9/2018. Cobra finish (26-STC, 5-Damages) on 02/11/2018.

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes		Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu	
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes		Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages), Pr	
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes		Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages). Pr	
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.	
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl	
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes		Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.	
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes		Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.	
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes		Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.	
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes		Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2	
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes		Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018	
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes		Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.	
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes		Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas	
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes		Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.	
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes		Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	70%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo	
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes		Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.	
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331	
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes		Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS		3	80%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig	
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes		Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done	
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	No						3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energiz	
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	0	0%	No						2/19/2018	6/15/2018	IN PROGRESS		7	45%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly	
39000	115	Toro Negro - Barranquitas	PREPA	5	0	0%	1	0	0%	No						3/24/2018	6/15/2018	IN PROGRESS		8	37%	Removed from FLUOR scope. Tower assembly	
36200	115	Daguao - Fajardo	PREPA	21	9	43%	12	6	50%	Yes		Yes	No	Yes	No	1/31/2018	7/31/2018	IN PROGRESS		9	4%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope. 06/01/2018 Pl	
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes		Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPFA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,	
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes		Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	45%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa	
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes		Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.	
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes		Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.	
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes		Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.	
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes		Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.	
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes		Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem	
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes		Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.	
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes		No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.	
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No						3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope	
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes		Yes	No			4/24/2018	TBD			20	0%	For rebuild.	
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes		Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.	
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes		Yes	No			2/24/2018	TBD			22	0%	For rebuild.	
				755	531		1237	966															

COBRA	7
PREPA	7
PENDING	3
	17



OVERALL PROGRESS
(As per completed Tasks)

TOTAL ENERGIZED

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNMENT	COMPLETED
PREPA	65	60	629	562
WHITEFISH	5	5	123	123
COBRA	17	11	813	610
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	89	1981	1549

Programa	Porcentaje
COBRA	43%
PREPA	36%
PENDING	21%

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%			
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages).		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages)		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to complete		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2/24/2018		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	13	100%	30	30	100%	Yes	Yes	No	Yes	No	10/17/2017	8/28/2018	COMPLETED	✓	2	100%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previous		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✓	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	3	100%	15	15	100%	Yes	Yes	No	Yes	No	1/28/2018	7/6/2018	COMPLETED	✓	3	100%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assigned		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	Yes					3/24/2018	5/31/2018	COMPLETED	✓	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018. Energize		
39000	115	Barranquitas - Comerio	PREPA	2	2	100%	8	6	75%	Yes			Yes	No	2/19/2018	9/8/2018	IN PROGRESS		7	82%	Reprioritized by PREPA on Dec 27, 2017. Pending of conductor works.		
39000	115	Toro Negro - Barranquitas	PREPA	5	5	100%	4	4	100%	Yes			Yes	No	3/24/2018	8/24/2018	COMPLETED	✗	8	100%	Removed from FLUOR scope. Line completed, pending of works at Toro Negro H.P.		
36200	115	Daguao - Fajardo	COBRA	12	0	0%	5	0	0%	Yes	Yes	No	Yes	No	7/31/2018	10/8/2018	IN PROGRESS		9	15%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope (9-STC, 6-Dar		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	Line work completed. Pending of OCB 36110 conduits replacement (ETC 9/21/2018)		
36300	115	Rio Blanco - Humacao	COBRA	26	16	62%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	9/5/2018	IN PROGRESS		11	89%	Removed from FLUOR scope. Assigned to COBRA. Working on tower installation.		
36300	115	Jobos - Maunabo	COBRA	51	16	31%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	9/29/2018	IN PROGRESS		12	66%	Removed from FLUOR scope. Assigned to COBRA. Working on tower installation.		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	9/23/2018	IN PROGRESS		13	95%	Reprioritized by PREPA.		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	10/23/2018	IN PROGRESS		14	27%	Removed from FLUOR. Assigned to COBRA. Working on access and poles installation.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	Removed from FLUOR. Assigned to PREPA.		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	9/30/2018	IN PROGRESS		17	66%	Removed from COBRA. Assigned to PREPA. Working on assessment and access.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	11/15/2018			18	11%	Spans damaged. Working on assessment and access.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	10/10/2018			19	0%	Removed from FLUOR scope. Assigned to COBRA.		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				746	546		1235	1003															

COBRA	6
PREPA	5
PENDING	3
	14



(kV)		
230	15	TOTAL ENERGIZED
115	67	
%	80%	

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNMENT	COMPLETED
PREPA	66	58	657	551
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	85	1992	1488

Actividad	Porcentaje
COBRA	39%
PREPA	44%
PENDING	17%

				Structures Repaired			Other Damage Repaired			Assessment		1149 Process		Wire Stringing									
Line	Voltage (kV)	Task Name	Resource	Structures Down	Structures Repaired	% Structures Repaired	Other Damage	Other Damage Repaired	% Other Damage Repaired	Detailed Assessment complete	Assessment Expected Completion	Issued 1149 and/or BOM to USACE/PREPA	Fulfilled 1149/BOM USACE PREPA	Wire Stringing Required (Yes or No)	Wire Stringing Completed (Yes or No)	Start	Proposed Finish						
37700	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		Yes	-	-	-	9/22/2017	9/22/2017	COMPLETED	✓	-	100%	n/a	
37600	115	Palo Seco S.P. - Bayamon TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/23/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38500	115	San Juan S.P. - Hato Rey TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/26/2017	9/26/2017	COMPLETED	✓	-	100%	n/a	
40300	115	Pattern - Sta. Isabel TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/23/2017	9/26/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
40300	115	Ponce TC - Pattern	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/23/2017	9/27/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37100	115	S. German - Acacias	PREPA	0	0	n/a	2	2	100%	Yes		-	-	-	-	9/28/2017	9/28/2017	COMPLETED	✓	-	100%	n/a	
50300	230	Aguirre S.P. - Costa Sur S.P.	PREPA	0	0	n/a	12	12	100%	Yes		-	-	-	-	9/23/2017	9/28/2017	COMPLETED	✓	-	100%	n/a	
50400	230	Costa Sur S.P. - Mayaguez TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/28/2017	9/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36900	115	Canas TC - Ponce TC	PREPA	0	0	n/a	4	4	100%	Yes		-	-	-	-	9/29/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51100	230	Costa Sur S.P. - EcoElectrica	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	9/30/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51200	230	Costa Sur S.P. - Cambalache TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	9/27/2017	9/30/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36900	115	Costa Sur S.P. - Canas TC	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	9/27/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
39100	115	Cambalache TC - Hatillo TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/1/2017	10/1/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
51300	230	Costa Sur S.P. - Ponce TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	9/29/2017	10/1/2017	COMPLETED	✓	-	100%	n/a	
37200	115	Anasco TC - Aguadilla TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	10/2/2017	10/2/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36700	115	Mayaguez TC - S. Sebastian TC	PREPA	0	0	n/a	10	10	100%	-		-	-	-	-	10/3/2017	10/4/2017	COMPLETED	✓	-	100%	n/a	
39800	115	Mayaguez TC - Acacias TC	PREPA	0	0	n/a	1	1	100%	-		-	-	-	-	9/28/2017	10/4/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36100	115	Bayamon TC - Caná	PREPA	6	6	100%	4	4	100%	Yes		-	-	-	-	9/27/2017	10/5/2017	COMPLETED	✓	-	100%	n/a	
37200	115	Mayaguez TC - Anasco TC	PREPA	1	1	100%	4	4	100%	Yes		-	-	-	-	10/4/2017	10/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36100	115	Caná - Piñas TC	PREPA	7	7	100%	7	7	100%	Yes		-	-	-	-	9/30/2017	10/8/2017	COMPLETED	✓	-	100%	n/a	
36100	115	Monterrey TC - Unibon TC/Corozal	PREPA	0	0	n/a	2	2	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	n/a	
36100	115	Piñas TC - Monterrey TC	PREPA	1	1	100%	3	3	100%	-		-	-	-	-	10/9/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36300	115	Yabucoa - Humacao	PREPA	1	1	100%	1	1	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
41000	115	Yabucoa - Humacao	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	10/7/2017	10/13/2017	COMPLETED	✓	-	100%	Lightning arrester replaced. Tested OK.	
41500	115	Dorado TC - Piñas TC	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	9/26/2017	10/14/2017	COMPLETED	✓	-	100%	n/a	
38900	115	Berwind - Escorial	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38900	115	Escorial - Sabana Llana	PREPA	0	0	n/a	0	0	n/a	-		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a	
39000	115	Ponce TC - Juana Diaz TC	PREPA	0	0	n/a	1	1	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	n/a	
39100	115	Aguadilla TC - Mora TC	PREPA	0	0	n/a	9	9	100%	Yes		-	-	-	-	10/11/2017	10/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
36200	115	MTC - Villa Betina	PREPA	0	0	n/a	6	6	100%	-		-	-	-	-	10/13/2017	10/18/2017	COMPLETED	✓	-	100%	n/a	
38300	115	SJSP - Cachete	PREPA	1	1	100%	6	6	100%	Yes		-	-	-	-	10/11/2017	10/20/2017	COMPLETED	✓	-	100%	n/a	
38900	115	Martin Pena - Berwind	PREPA	13	13	100%	3	3	100%	Yes		-	-	-	-	9/27/2017	10/22/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
50900	230	Aguas Buenas - BTC	PREPA	3	3	100%	0	0	0%	Yes		-	-	-	-	9/28/2017	10/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable	
39000	115	Aguas Buenas - Caguas TC	PREPA	0	0	n/a	5	5	100%	Yes		-	-	-	-	10/26/2017	10/29/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
39000	115	Comerio - Aguas Buenas	PREPA	1	1	100%	5	5	100%	Yes		-	-	-	-	11/1/2017	11/4/2017	COMPLETED	✓	-	100%	n/a	
40100	115	Aguirre S.P. - Jobos	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	9/27/2017	11/5/2017	COMPLETED	✓	-	100%	n/a	
37400	115	Vega Baja - Manati	PREPA	2	2	100%	3	3	100%	Yes		-	-	-	-	10/20/2017	11/6/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38100	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a	
38400	115	SJSP - Viaducto	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	n/a	
38800	115	Hato Rey - Viaducto	PREPA	0	0	n/a	0	0	n/a	Yes		-	-	-	-	11/9/2017	11/11/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37400	115	Hato Tejas TC - Candelaria Arenas TC	PREPA	1	1	100%	0	0	0%	-		-	-	-	-	11/2/2017	11/15/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37400	115	Bayamon TC - Orea TC	PREPA	2	2	100%	4	4	100%	Yes		-	-	-	-	10/31/2017	11/21/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable	
37900	115	Encantada - Sabana Llana	PREPA	1	1	100%	7	7	100%	Yes		-	-	-	-	11/10/2017	11/27/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable	
36400	115	Jayuya - Dos Bocas	PREPA	5	5	100%	1	1	100%	Yes		-	-	-	-	11/10/2017	11/28/2017	COMPLETED	✓	-	100%	n/a	
37900	115	Conquistador - Encantada	PREPA	4	4	100%	0	0	0%	Yes		-	-	-	-	11/3/2017	12/5/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37400	115	Crea TC - Hato Tejas TC	PREPA	1	1	100%	3	3	100%	Yes		-	-	-	-	11/9/2017	12/14/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37400	115	Dos Bocas - Cambalache	PREPA	1	1	100%	10	10	100%	Yes		-	-	-	-	11/18/2017	12/16/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
39000	115	Juana Diaz - Toro Negro	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	No	No	12/4/2017	12/23/2017	COMPLETED	✓	-	100%		
36100	115	Unibon TC - Morovis	PREPA	8	8	100%	4	4	100%	Yes		Yes	Yes	Yes	No	11/20/2017	12/24/2017	COMPLETED	✓	-	100%		
36100	115	Morovis - Ciales	PREPA	16	16	100%	7	7	100%	Yes		Yes	Yes	Yes	No	12/6/2017	12/30/2017	COMPLETED	✓	-	100%		
51000	230	Aguas Buenas - Sabana Llana	PREPA	5	5	100%	17	17	100%	Yes		Yes	Yes	Yes	No	10/28/2017	1/14/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
37100	115	Costa Sur S.P. - Guanica	PREPA	4	4	100%	6	6	100%	Yes		-	-	-	-	1/27/2018	2/9/2018	COMPLETED	✓	-	100%	WX Permitting.	
37100	115	Guanica - S. German	PREPA	2	2	100%	18	18	100%	Yes		-	-	-	-	2/14/2018	2/16/2018	COMPLETED	✓	-	100%		
50200	230	Manati - Costa Sur S.P.	PREPA	4	4	100%	14	14	100%	Yes		Yes	Yes	Yes	No	11/29/2017	2/25/2018	COMPLETED	✓	-	100%	PREPA finish on 2/20/2018. Cobra complete conductor installation (2-Damages) on 2/21/18	
37400	115	Candelaria Arenas TC - Dorado TC	PREPA	11	11	100%	0	0	0%	Yes		Yes	Yes	Yes	No	12/18/2017	3/14/2018	COMPLETED	✓	-	100%	Two poles pending to be installed (Super Puma). Proposed finish date was 2/18/2018. (	
37400	115	Dorado TC - Vega Baja	PREPA	14	14	100%	22	22	100%	Yes		Yes	Yes	Yes	No	1/16/2018	3/27/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Proposed finish date was 3/3/2018. Cobra is working (3-ST	
50100	230	Cambalache TC - Manati	WHITEFISH	2	2	100%	39	39	100%	Yes		-	-	-	-	10/13/2017	10/25/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
50200	230	Manati - BTC	WHITEFISH	4	4	100%	19	19	100%	Yes		-	-	-	-	10/14/2017	10/29/2017	COMPLETED	✓	-	100%	n/a	
37400	115	Manati - Barceloneta	WHITEFISH	8	8	100%	8	8	100%	Yes		-	-	-	-	10/19/2017	11/14/2017	COMPLETED	✓	-	100%	n/a	
50900	230	Aguirre S.P. - Aguas Buenas	WHITEFISH	9	9	100%	9	9	100%	Yes		-	-	-	-	10/11/2017	11/29/2017	COMPLETED	✓	-	100%	Energized without replacing damaged OPGW cable	
36200	115	Villa Betina - Juncos	WHITEFISH	6	6	100%	19	19	100%	Yes		-	-	-	-	10/23/2017	11/30/2017	COMPLETED	✓	-	100%		
38300	115	Monacillos - Cachete	NYPA	0	0	n/a	0	4	100%	Yes		-	-	-	-	11/16/2017	11/20/2017	COMPLETED	✓	-	100%	n/a	
38600	115	San Juan S.P. - BTC	NYPA	0	0	n/a	8	8	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
38700	115	San Juan S.P. - Palo Seco S.P.	NYPA	0	0	n/a	3	3	100%	Yes		-	-	-	-	11/21/2017	12/3/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
50700	230	Aguirre S.P. - Guayama / A.E.S.	COBRA	5	5	100%	12	12	100%	Yes		-	-	-	-	10/31/2017	12/7/2017	COMPLETED	✓	-	100%	OPGW installed. Tested OK.	
37800	115	Cayey - Jobos/Guayama	COBRA	2	2	100%	27	27	100%	Yes		Yes	No	Yes	Yes	11/10/2017	12/0/2018	COMPLETED	✓	-	100%	Sleeves issue. Waiting on material, change to 1/17/18 pending material delivery	
41400	115	Humacao - Juncos	COBRA	34	34	100%	17	17	100%	Yes		Yes	Yes	Yes	Yes	12/7/2017	2/21/2018	COMPLETED	✓	-	100%	Masterc finish (8-STC, 12-D	

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes	Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu		
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes	Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr		
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes	Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPA Finish (18-STC, 46-Damages). Pr		
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.		
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes	Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.		
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes	Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl		
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes	Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.		
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes	Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA02/8/2018.		
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes	Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.		
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes	Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2		
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes	Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018		
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes	Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.		
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes	Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas		
50700	230	Gua yama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes	Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGW partially installed.		
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes	Yes	No	Yes	No	10/17/2017	6/1/2018	IN PROGRESS		2	70%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo		
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes	Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.		
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes	Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending.		
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes	Yes	No	Yes	No	1/28/2018	6/1/2018	IN PROGRESS		3	80%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig		
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes	Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done		
39000	115	Aguas Buenas - MTC	PREPA	2	0	0%	7	0	0%	No					3/24/2018	6/1/2018	IN PROGRESS		6	95%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	0	0%	No					2/19/2018	6/15/2018	IN PROGRESS		7	40%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly		
39000	115	Toro Negro - Barranquitas	PREPA	5	0	0%	1	0	0%	No					3/24/2018	6/15/2018	IN PROGRESS		8	35%	Removed from FLUOR scope. Tower assembly		
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes	Yes	Yes	Yes	No	3/4/2018	TBD			9	85%	Reprioritized by PREPA.		
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes	Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,		
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes	Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	45%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa		
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes	Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.		
36200	115	Daguao - Fajardo	PREPA	21	9	43%	12	6	50%	Yes	Yes	No	Yes	No	1/31/2018	TBD	IN PROGRESS		13	17%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope. 05/21/2018 P		
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes	Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUOR scope.		
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes	Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.		
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes	Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem		
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes	Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.		
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes	No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.		
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No					3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUOR scope		
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes	Yes	No			4/24/2018	TBD			20	0%	For rebuild.		
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes	Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.		
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes	Yes	No			2/24/2018	TBD			22	0%	For rebuild.		
				755	529		1237	959															

COBRA	7
PREPA	8
PENDING	3
	18



(kV)		
230	15	TOTAL ENERGIZED
115	67	
%	80%	

	TOTALS BY RESOURCE		TOTALS BY DAMAGE ASSIGNED	
	LINE SEGMENT	COMPLETED	ASSIGNMENT	COMPLETED
PREPA	66	59	657	560
WHITEFISH	5	5	123	123
COBRA	16	9	796	560
NYPA	3	3	15	15
Fluor/PIKE	6	6	109	109
Fluor/ARC	1	1	27	27
Fluor/MasTec	0	0	0	0
Fluor/SEC	1	1	25	25
USACE/PowerSecure	2	2	32	32
Pending-RFP	3	0	208	46
Totals	103	86	1992	1497

Status	Percentage
COBRA	41%
PREPA	41%
PENDING	18%

[illegible]

50800	230	Yabucoa - Sabana Llana	COBRA	7	7	100%	107	107	100%	Yes		Yes	Yes	Yes	No	12/5/2017	2/27/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Cobra finish (3-STC, 66-Damages) on 2/15/2018. Flu	
37500	115	MTC - Grana	COBRA	7	7	100%	21	21	100%	Yes		Yes	No			11/30/2017	3/31/2018	COMPLETED	✓	-	100%	NYPFA Finish (4-STC, 16-Damages) on 2/7/2018. Cobra is working (3-STC, 5-Damages). Pr	
38200	115	Palo Seco S.P. - MTC	COBRA	18	18	100%	48	48	100%	Yes		Yes	No	Yes	No	11/29/2017	3/31/2018	COMPLETED	✓	-	100%	Tested OK. Eliminated 6 wood Stc. by using Steel Stc. NYPFA Finish (18-STC, 46-Damages). Pr	
41200	115	Sabana Llana - Canovanas	Fluor/PIKE	5	5	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/6/2018	COMPLETED	✓	-	100%	OPGW installed. Currently working to replace damaged OPGW spans.	
36800	115	Sabana Llana - Canovanas	Fluor/PIKE	6	6	100%	8	8	100%	Yes		Yes	Yes	Yes	Yes	11/28/2017	1/22/2018	COMPLETED	✓	-	100%	Telecommunications advised that OPGW will be included.	
36800	115	Canovanas - Palmer	Fluor/PIKE	35	35	100%	9	9	100%	Yes		Yes	Yes	Yes	Yes	11/1/2017	2/28/2018	COMPLETED	✓	-	100%	OPGW installed. Spans damaged. Few structures need rework. 3/8/18- Need to compl	
37800	115	MTC - Buen Pastor	Fluor/PIKE	6	6	100%	10	10	100%	Yes		Yes	Yes	Yes	No	12/11/2017	3/7/2018	COMPLETED	✓	-	100%	Proposed Finish date was 2/14/2018 and 2/28/2018. Turnover to PREPA 02/23/2018.	
38900	115	Hato Rey - Martin Pena	Fluor/PIKE	11	11	100%	4	4	100%	Yes		Yes	Yes	Yes	Yes	12/21/2017	3/11/2018	COMPLETED	✓	-	100%	OPGW installed. Tested OK. Turnover to PREPA 02/8/2018.	
36200	115	Juncos - Rio Blanco	Fluor/ARC	7	7	100%	20	20	100%	Yes		Yes	Yes	Yes	No	11/3/2017	3/19/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/18/2018. Turnover to PREPA 02/27/2018.	
36300	115	Shell TC/Juan Martin Sect. - Yabucoa	Fluor/SEC	6	6	100%	19	19	100%	Yes		Yes	No	Yes	No	1/16/2018	3/16/2018	COMPLETED	✓	-	100%	QA/QC. Multiple segments. Cobra working the first 3-STC. Proposed finish date was 2	
37200	115	Mayaguez GP - Mayaguez TC	USACE/PowerSecure	2	2	100%	10	10	100%	Yes		Yes	Yes			2/10/2018	2/21/2018	COMPLETED	✓	-	100%	Proposed Finish Date was 2/24/2018	
50500	230	Mora - Mayaguez TC	USACE/PowerSecure	1	1	100%	19	19	100%	Yes		Yes	Yes			2/10/2018	3/3/2018	COMPLETED	✓	-	100%	PREPA priority.	
36500	115	Dos Bocas - Caonillas	Fluor/PIKE	4	4	100%	2	2	100%	Yes		Yes	Yes	No	No	2/7/2018	2/19/2018	COMPLETED	✗	-	100%	Test failed. Inspected by District 04/25/2018. Waiting for materials and repair, Dos Bocas	
50700	230	Guayama / A.E.S. - Yabucoa	COBRA	53	53	100%	80	80	100%	Yes		Yes	Yes	Yes	No	12/4/2017	4/17/2018	COMPLETED	✓	1	100%	COBRA/PREPA-OPGWpartially installed.	
51000	230	Aguirre S.P. - Aguas Buenas	COBRA	13	10	77%	30	2	7%	Yes		Yes	No	Yes	No	10/17/2017	6/29/2018	IN PROGRESS		2	70%	WFISH/COBRA-Cobra new line. WF and PREPA working a portion of this segment previo	
40200	115	Aguirre S.P. - Jobos	COBRA	17	17	100%	20	20	100%	Yes		Yes				1/30/2018	4/23/2018	COMPLETED	✓	2.1	100%	QA/QC done, Line tested ok.	
40300	115	Sta. Isabel TC - Aguirre	COBRA	3	3	100%	6	6	100%	Yes		Yes	No			2/25/2018	5/30/2018	COMPLETED	✗	2.2	100%	OPGW installed. Proposed finish date 06/01/18. Aguirre control work pending BKR 40331	
36300	115	Maunabo - Shell/Juan Martin Sect.	COBRA	3	2	67%	15	10	67%	Yes		Yes	No	Yes	No	1/28/2018	6/30/2018	IN PROGRESS		3	80%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope. Assig	
36800	115	Palmer - Fajardo	PREPA	12	12	100%	10	10	100%	Yes		Yes	No	Yes	No	1/28/2018	5/10/2018	COMPLETED	✓	5	100%	FLUOR/PREPA-Removed from FLUOR scope. Assigned to PREPA April 2018. QA/QC done	
39000	115	Aguas Buenas - MTC	PREPA	2	2	100%	7	7	100%	No						3/24/2018	5/31/2018	COMPLETED	✗	6	100%	OPGW installed. Removed from FLUOR scope. Proposed finish date 06/01/2018.	
39000	115	Barranquitas - Comerio	PREPA	2	0	0%	6	0	0%	No						2/19/2018	6/15/2018	IN PROGRESS		7	42%	Reprioritized by PREPA on Dec 27, 2017. Tower assembly	
39000	115	Toro Negro - Barranquitas	PREPA	5	0	0%	1	0	0%	No						3/24/2018	6/15/2018	IN PROGRESS		8	32%	Removed from FLUOR scope. Tower assembly	
36200	115	Daguao - Fajardo	PREPA	21	9	43%	12	6	50%	Yes		Yes	No	Yes	No	1/31/2018	TBD	IN PROGRESS		9	1%	FLUOR/PREPA-Proposed finish was 4/3/2018. Removed from FLUOR scope. 06/01/2018 Pl	
36100	115	Monacillos - BTC	PREPA	18	18	100%	19	19	100%	Yes		Yes	Yes	Yes	No	1/10/2018	5/7/2018	COMPLETED	✗	10	100%	NYPFA/COBRA/PREPA-Six lane highway crossing to coordinate. Cobra is working (3-STC,	
36300	115	Rio Blanco - Humacao	COBRA	26	7	27%	12	5	42%	Yes		Yes	Yes	Yes	No	11/3/2017	7/15/2018	IN PROGRESS		11	45%	FLUOR/COBRA-Cobra Finish (5-STC, 1-Damages) on 02/21/2018. Proposed finish date wa	
36300	115	Jobos - Maunabo	COBRA	51	12	24%	67	16	24%	Yes		Yes	No	Yes	No	1/28/2018	7/15/2018	IN PROGRESS		12	40%	FLUOR/COBRA-Proposed finish date was 2/28/2018. Removed from FLUOR scope.	
37400	115	Barceloneta - Cambalache	PREPA	11	5	45%	6	0	0%	Yes		Yes	Yes	Yes	No	3/4/2018	TBD			13	85%	Reprioritized by PREPA.	
36200	115	Rio Blanco - Daguao	COBRA	22	6	27%	23	6	26%	Yes		Yes	No	Yes	No	1/18/2018	7/15/2018	IN PROGRESS		14	27%	FLUOR/COBRA-Removing grounds. Removed from FLUORscope.	
37800	115	Caguas - Cayey	PREPA	15	3	20%	21	4	19%	Yes		Yes	Yes	Yes	No	1/24/2018	TBD			15	23%	FLUOR/PREPA-Removed from FLUOR scope.	
37800	115	Buen Pastor - Caguas	PREPA	42	40	95%	33	31	94%	Yes		Yes	Yes	Yes	No	11/1/2018	TBD			16	95%	FLUOR/PREPA-Waiting - need 20K ft. static wire - May energize & install static later. Rem	
50500	230	Mora - Cambalache	PREPA	1	0	0%	39	20	51%	Yes		Yes	No			2/10/2018	TBD			17	66%	P-SECURE/PREPA-Proposed finish date was 3/24/2018. Turnover to PREPA 03/29/2018.	
37900	115	MTC - Conquistador	COBRA	15	0	0%	20	0	0%	Yes		No				2/21/2018	TBD			18	5%	OPGW installed. Spans damaged. Waiting Flyover assessment.	
37000	115	Costa Sur SP - Ponce TC	COBRA	10	0	0%	5	0	0%	No						3/16/2018	TBD			19	0%	OPGW installed. Spans damaged. Gathering information. Removed from FLUORscope	
36400	115	Ponce TC - Jayuya	PENDING-RFP	45	0	0%	30	0	0%	Yes		Yes	No			4/24/2018	TBD			20	0%	For rebuild.	
36100	115	Ciales - Dos Bocas	PENDING-RFP	22	16	73%	41	30	73%	Yes		Yes	Yes	No	No	1/14/2018	TBD			21	72%	For rebuild.	
36600	115	San Sebastian - Dos Bocas	PENDING-RFP	30	0	0%	40	0	0%	Yes		Yes	No			2/24/2018	TBD			22	0%	For rebuild.	
				755	531		1237	966															

COBRA	7
PREPA	7
PENDING	3
	17




Energy Sector


HIGH FOCUS AREA

- Continue focus on completion of emergency work; develop PWs for permanent work. Payments to IOUs, NYS, and Cobra are outstanding; we are addressing with Commonwealth and PREPA.

CATEGORY A & B OVERVIEW

PA Spend Plan Projections as of 06/06/2018
Obligations as of 06/25/2018

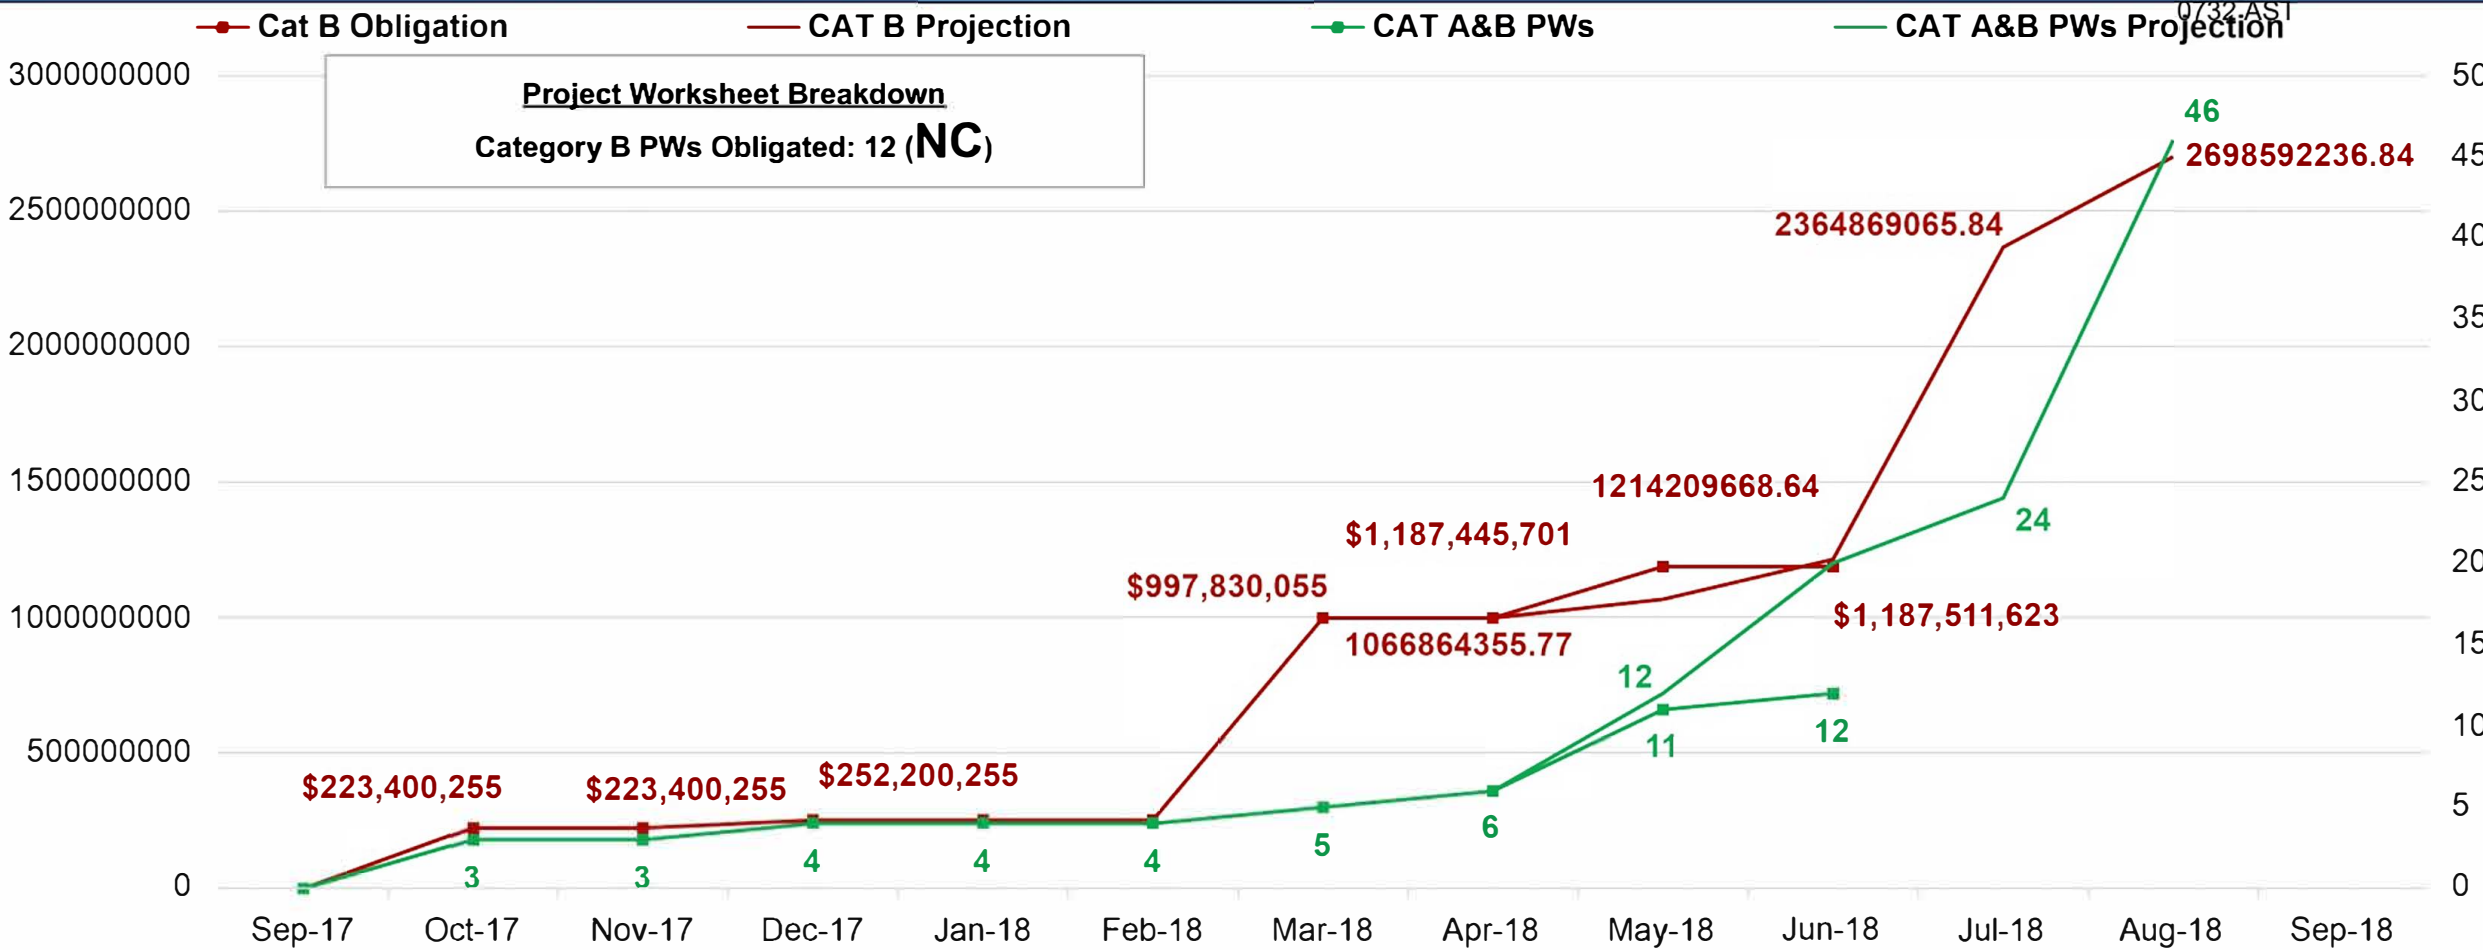



REBUILDING PUERTO RICO ENERGY SECTOR

May 10, 2018

Task Force Power Restoration

Power Restoration Visualization




USACE this together to show how restoration was achieved and the time it took. This loop is from November to May.

The map begins to brighten up, but we still see those pockets we have yet to reach.

And let me make this point....while we are talking today about rebuilding, let me be clear! We are NOT NOT NOT turning our back to the 1.56% of the customers that still do not have power.

We will continue to work just as hard on that restoration while we are looking ahead to our future...an amazing opportunity for the people of Puerto Rico, PREPA, and the Commonwealth.

So I want to take a few minutes to show how we got here and the complexity of this restoration

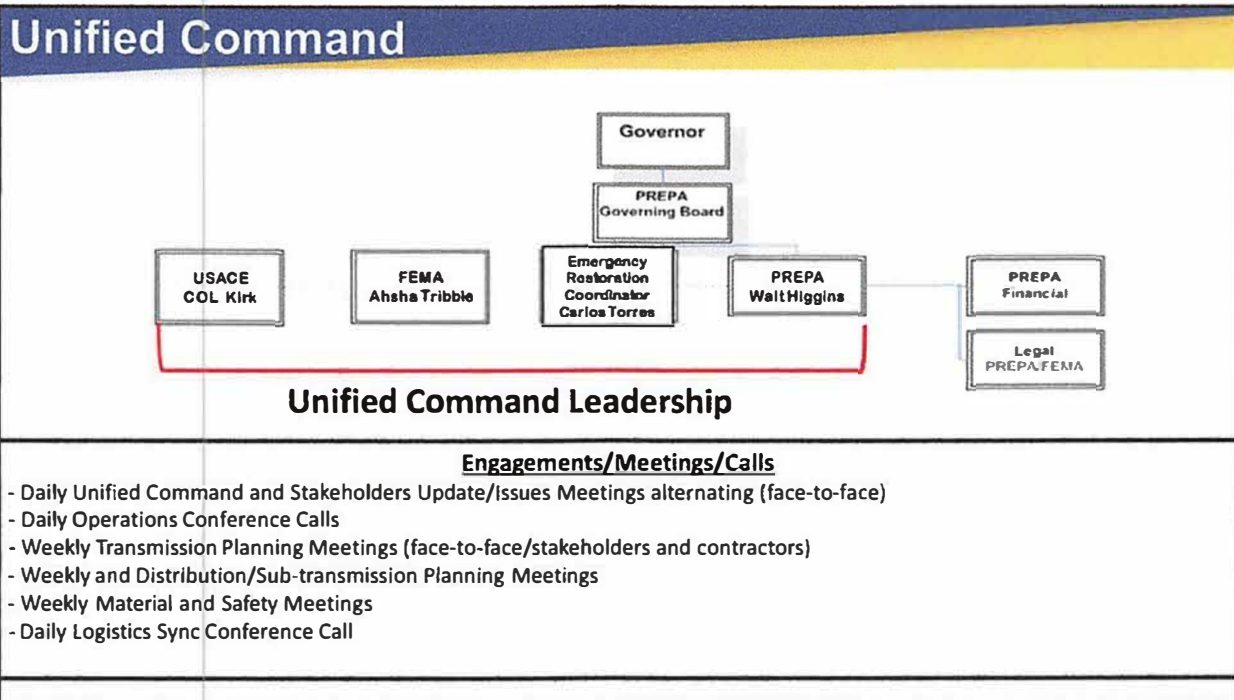


Because we gave a Mission Assignment to USACE, PREPA had its contractors, and the Gov's Island Restoration coordination.

We needed a process for **unity effort and unity of message**.

We met everyday, 7 days a week for 6 months.

FEMA –forever meeting agency

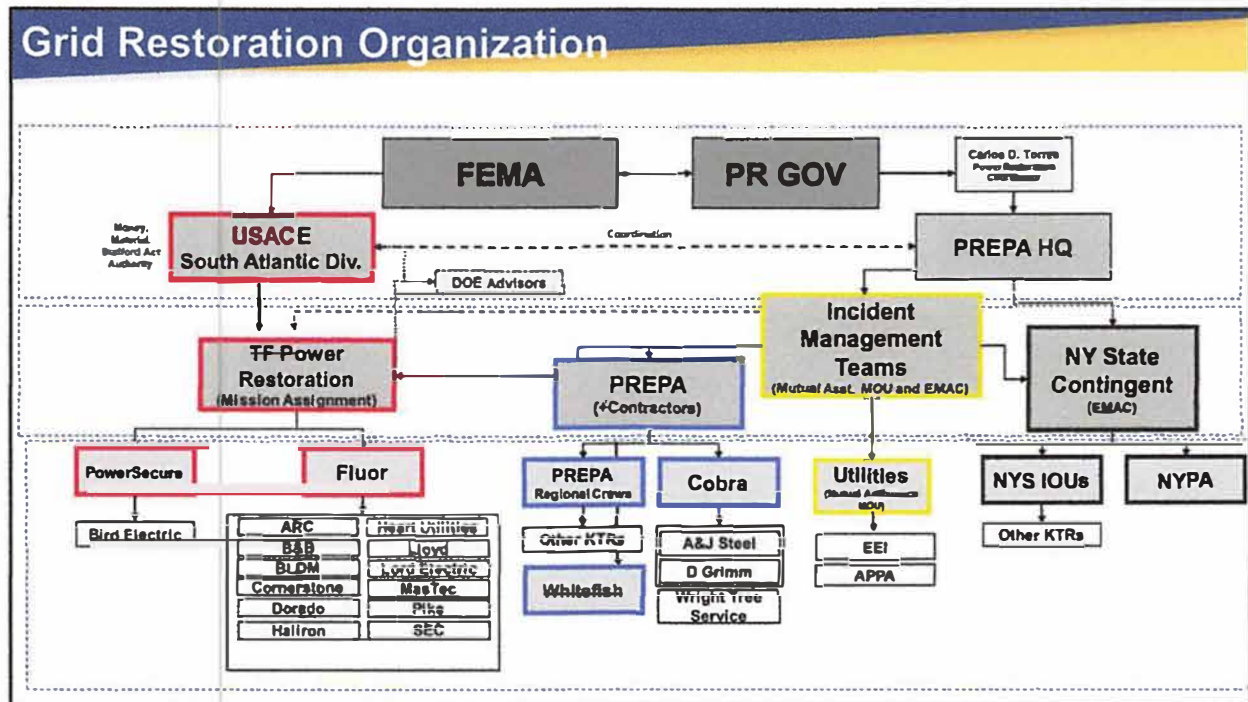

Here is why it was so complicated

USACE – Mission Assignment

PREPA Contractors – PA Reimbursement

IOUs under a Memorandum of Understanding

NY State Contingent under EMAC

Consideration for where crews lived (Life support)

Where they were going to work...if you moved them,
increase windshield time

Laydown Yards

Materials management

Transmission or distribution?

Helicopter, Drone, bucket truck?

Wood, steel, or concrete pole...just because you can
work one doesn't mean you can work the
other....gloved, hot stick trailer...



Layer on the 8 Incident Management Teams from Industry (planning, ops, safety, log, ...)

They really kept us to task, especially when we had all of the IOUs on island. It has the chance to be unwieldy and safety was always an issue

The road was bumpy at the beginning with these mainland folks coming to help manage an operation. But it worked out, and we felt it when they left.


IT WAS COMPLEX...

Restoration Support to PREPA			
GENERATION	TRANSMISSION	SUBSTATIONS	DISTRIBUTION (+ Sub-Transmission)
	   	 	    

My favorite slide as it debunks media and congressional criticism of operations on the ground and what was really needed

NEEDED CONTRACTORS

To all of you, I thank you for your sacrifice, leaving families, and embedding with the community.

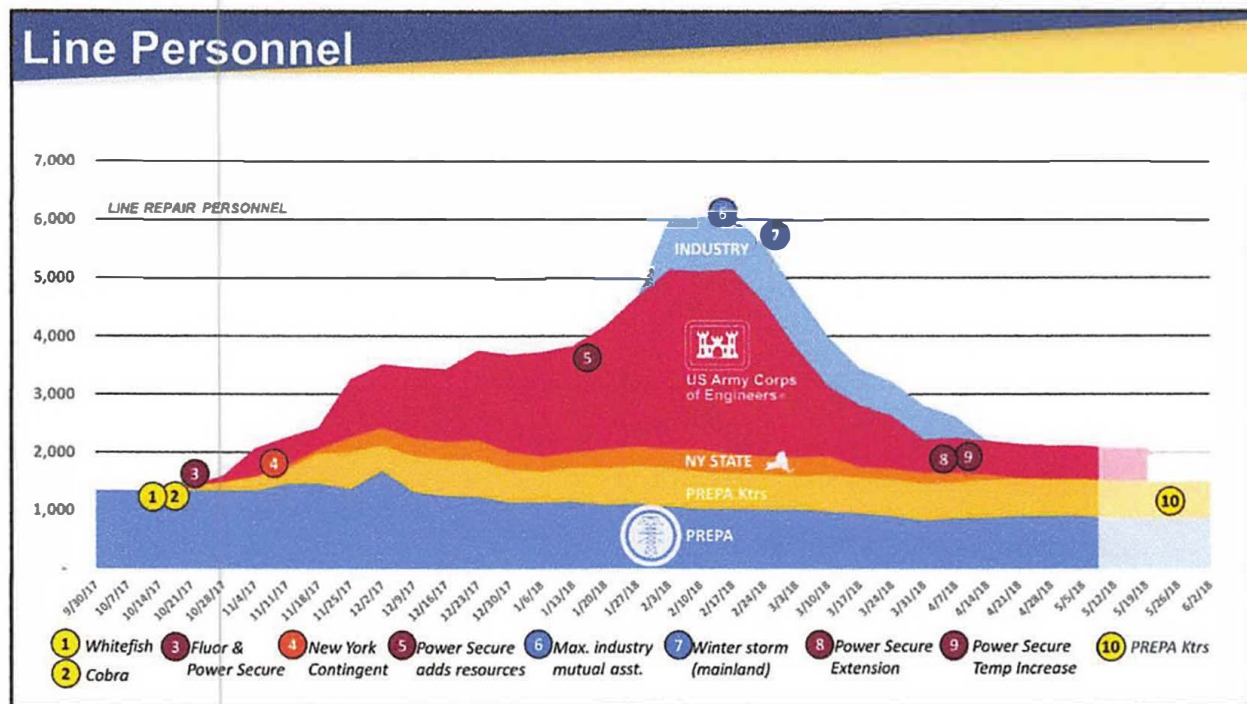

It took time to get mobilized...barges, space a ports, lodging, life support

Cobra lived on two barges and had the hardest hit part of the island and most of the transmission worked so that worked for them.

PowerSecure had the western portion of the island Mayaguez and had really neat travel trailers and that worked for them.

Creativity was the name of the game.

Where we are today?



GOVERNMENT OF PUERTO RICO

COR



FEMA

Municipality Map

98.47% restored; 1.53% remaining
22,562 customers still without power



Porcentos en servicio



*El porcentaje indicado en los municipios representa el porcentaje aproximado de clientes en servicio a nivel de comunidad de dicho municipio en base al total de clientes en el municipio

RESUMEN MUNICIPAL

As long as people don't have power, we are not satisfied.

Current Focus

- 1) Restoring the remaining 1.56% of customers
- 2) Transitioning management of the restoration back to PREPA for completion
- 3) Preparation for upcoming hurricane season




Restoring the remaining 1.53% of customers

Transitioning management of the restoration back to PREPA for completion

Preparation for upcoming hurricane season

NO!



1) Restoring the remaining
1.53% of the

2) The remaining management
of the remaining 1.53% of the
for the remaining 1.53%

3) The remaining management
of the remaining 1.53% of the

Restoring the remaining 1.53% of
the remaining 1.53% of the

Restoring the remaining management of the
remaining 1.53% of the remaining 1.53% of the

Restoring the remaining management of the
remaining 1.53% of the remaining 1.53% of the

Restoring the remaining management of the
remaining 1.53% of the remaining 1.53% of the

Restoring the remaining management of the
remaining 1.53% of the remaining 1.53% of the

Where are we going?



LEO LANG & ASSOCIATES

COR

 **FEMA**

Vision Statement

Deliver a modern, reliable, and resilient power system for the people and businesses of Puerto Rico to support an enduring economy and future-ready island.



GOVERNMENT OF PUERTO RICO

COR

 **FEMA**




Which brings us to one of the main objectives the summit!...The Energy Sector Solutions Team: to imagine holistic solutions for the entire energy infrastructure on the island.

It is made up of federal agencies, industry, and stakeholders...some will be permanent here on the island, and others will be remote.

They will challenge us. Find creative solutions. Engage experts. And keep us legal!

The goal is to have a team with access to the most effective, innovative, and cutting edge technologies to
build a future ready grid.

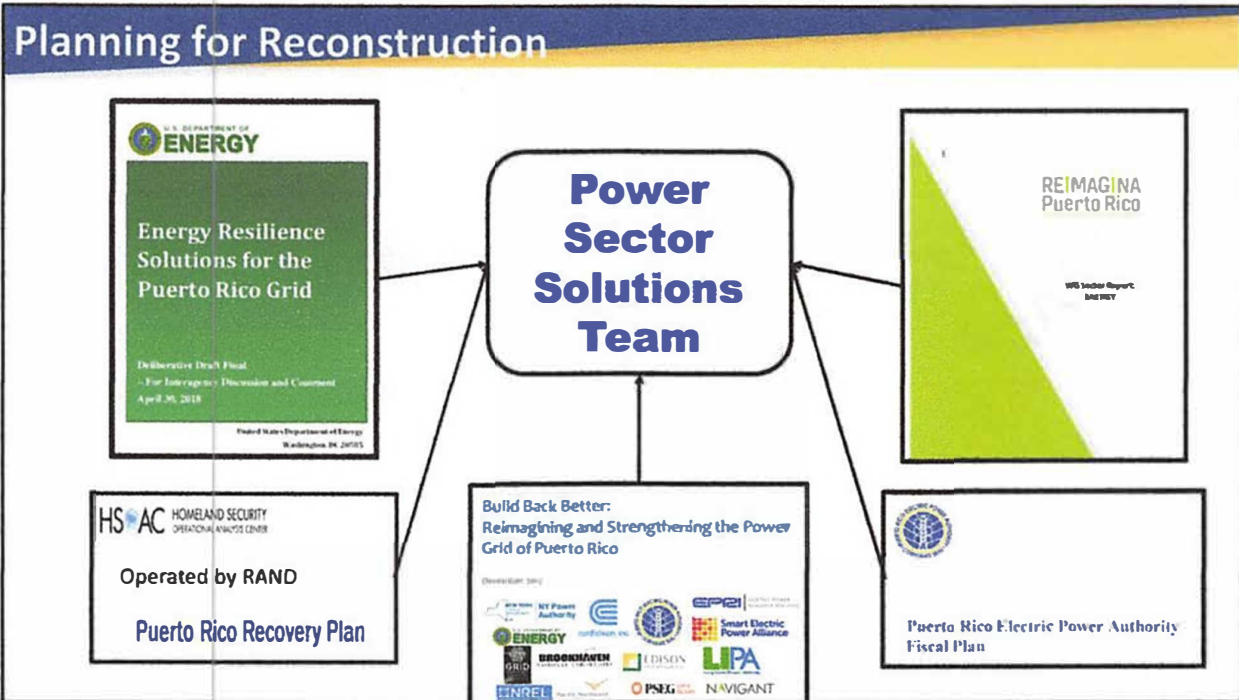

We will use reports that have been developed to support decision making such as these on the slide.

The Commonwealth, NY State and partners, RAND, DOE, 100 resilient cities, and others who have been thinking about the grid here in PR.

Begin Permanent Work

- Establish Solutions Team (co-lead by COR3 and FEMA)
- Review reports/Summit results
- Retain diverse design engineers
- Scoping early projects
 - Distribution System Vieques and Culebra
 - 230KV Loop around the mainland




GOVERNMENT OF PUERTO RICO

COR



FEMA



We will work together in support of the Commonwealth and do what is right for the businesses and people of Puerto Rico.

Again, I want to thank everyone for being here and **we look forward to your input and questions.**
